

Project Update

St. Pius X Catholic School

April 6, 2023



WE BUILD **GREAT**

SCHOOLS

INDUSTRIAL FACILITIES

HEALTHCARE FACILITIES

COMMUNITIES

LEADERS

FUTURES .



Table of Contents

- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



Owner	Architect/Engineer	Parrish Construction Group
<ul style="list-style-type: none">• Catholic Education of North Georgia, Inc.• St. Pius X Catholic High School	<ul style="list-style-type: none">• CDH Architecture	<ul style="list-style-type: none">• David Loudermilk, Project Director• Alex Johnson, Project Manager• Hoyt Clance, Superintendent• Trey DeRieux, Project Engineer• Drew Plunkett, Asst. Superintendent



PARRISH
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

SUMMARY REPORT

Critical Tasks	% Complete
SITEWORK	10%
FOUNDATIONS	0%
UNDERGROUND UTILITIES	0%
SLAB ON GRADE/DECK	0%
STEEL	0%
ELECTRICAL	0%
PLUMBING	0%
MECHANICAL	0%
ROOFING	0%



WEEKLY PROGRESS UPDATE

- INSTALLED STORM LINE AND STRUCTURES FROM B-1 TO B-5
- INSTALLED STORM LINE AND STRUCTURES FROM A-1 TO A-3
- PARKING LOT GRADING



SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Site Work		
GRADING AND UTILITIES	RUBY-COLLINS	10%
UNDERGROUND GAS LINE	POLK COUNTY PUBLIC SERVICE	0%
Building Systems		
MECHANICAL	GEORGIA MECHANICAL	0%
ELECTRICAL	ALL STATE ELECTRICAL CONTRACTORS	0%
PLUMBING	POLK COUNTY PUBLIC SERVICE	0%
FIRE PROTECTION	GAINESVILLE FIRE PROTECTION	0%
Building Structure		
FOUNDATION AND SLAB ON GRADE (SOG)	PARRISH CONCRETE	0%
STRUCTURAL STEEL FRAMING	TRINITY FABRICATORS	0%
EXTERIOR WALLS	PARRISH MASONRY	0%
INTERIOR WALLS	PARRISH MASONRY/HOLT & HOLT	0%



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Building Envelope		
BRICK	PARRISH MASONRY	0%
WINDOWS/STOREFRONT	COMMERCIAL GLASS & MIRRORS	0%
Building Interiors		
FLOORING	PERIMETER FLOORS	0%
DRYWALL	HOLT & HOLT	0%
CEILINGS	HOLT & HOLT	0%
PAINTING	MCS PAINTING	0%



PROJECT UPDATE

WE BUILD GREAT


THREE WEEK LOOK AHEAD

PROJECT UPDATE

WE BUILD GREAT

PARRISH
CONSTRUCTION GROUP

PROGRESS UPDATE

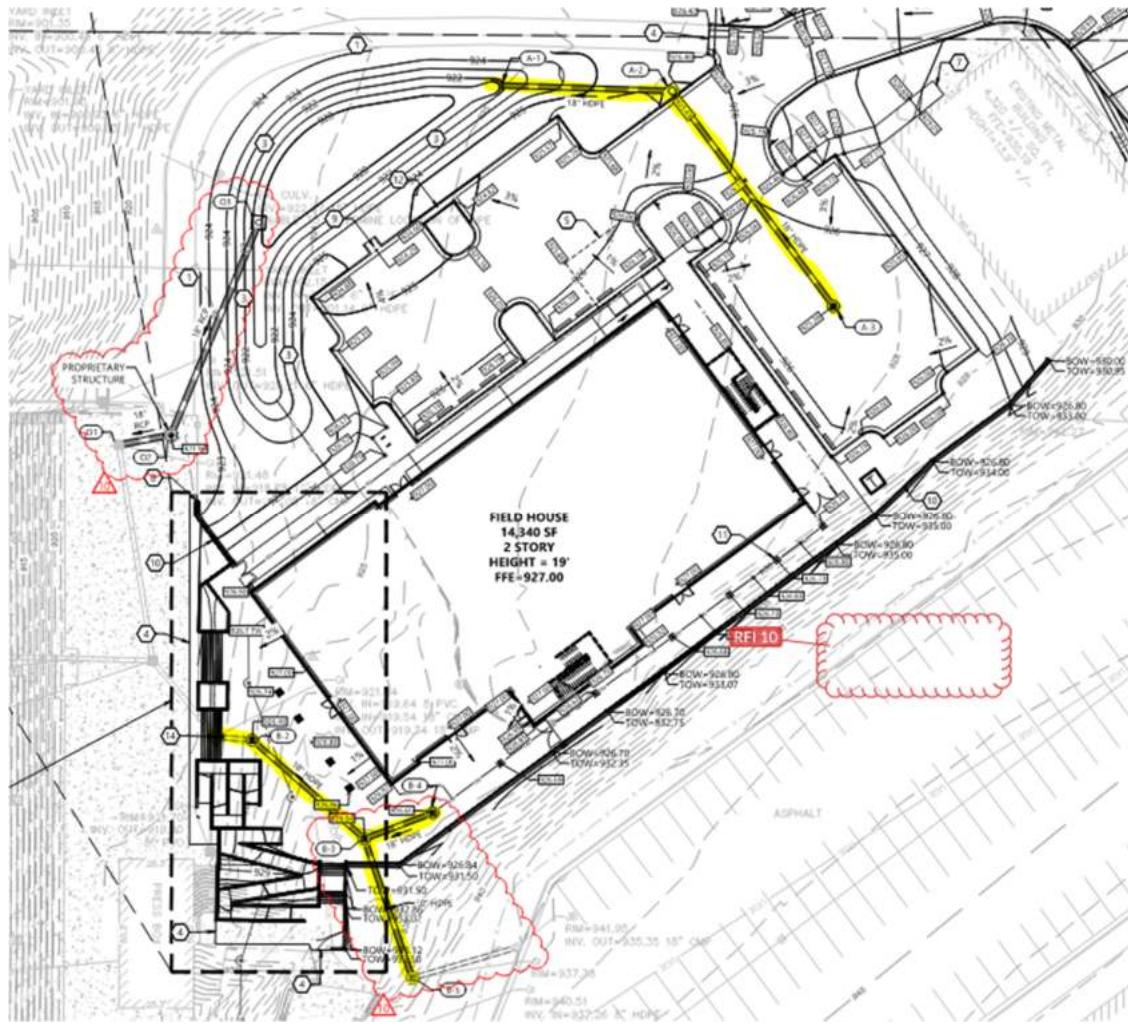

**HIGHLIGHTED SECTIONS HAVE
BEEN COMPLETED**

PROJECT PHOTOS

WE BUILD GREAT



PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS



ACOUSTICAL BAFFLES IN THE MEDIA CENTER



PROJECT PHOTOS

STRUCTURES B-1 AND B-2





PROJECT PHOTOS



**STORM LINE AND STRUCTURES FROM B-3
TO B-4**

PROJECT PHOTOS

WE BUILD GREAT



PROJECT PHOTOS



**STORM LINE AND STRUCTURES INSTALLED
FROM A-1 TO A-2**



PROJECT PHOTOS

STORM LINE INSTALLED FROM A-2 TO A-3



Contact Information



David Loudermilk

Project Director
478.256.1839

dloudermilk@parrishconstruction.com



Alex Johnson

Project Manager
470.540.0047

ajohnson@parrishconstruction.com



Hoyt Clance

Superintendent
478.244.6349

hclance@parrishconstruction.com



Trey DeRieux

Project Engineer
470.442.3169

tderieux@parrishconstruction.com



Drew Plunkett

Asst. Superintendent
678.215.5193

dplunkett@parrishconstruction.com

WE BUILD GREAT

SCHOOLS

INDUSTRIAL FACILITIES

HEALTHCARE FACILITIES

COMMUNITIES

LEADERS

FUTURES .
