

WEEKLY SUMMARY

November 2, 2018



Picture 1: Mary Beth's Future Office

DELAWARE AREA CAREER CENTER: SOUTH CAMPUS CONSOLIDATION OF FACILITIES

Construction Activities

Completed

- In-Wall Plumbing Inspection in the Dental Assisting, Exercise Science, and Fire Service Tech Labs
- In-Wall Blocking in the Biology and Chemistry Labs
- Hanging and Finishing of Drywall in Cosmetology
- Interior Wall Framing in the East Admin Area
- Startup of Rooftop Unit Serving Early Childhood Development

Ongoing

- Overhead HVAC, Electrical, and Technology Rough-In in Cosmetology, Fire Service Tech, and the Biology/Chemistry Labs
- Finishing of Drywall in Early Childhood Development
- Exterior Masonry in the East Admin Area
- Hanging of Drywall in the Exercise Science, Dental Assisting, and Biology/Chemistry Labs
- Interior Wall Framing in the Academic Learning Commons Classrooms
- Insulating of Hydronic Piping in Early Childhood Development and the Dental Assisting, Biology/Chemistry, and Exercise Science Labs

Upcoming


- Hanging of Drywall and Installation of Hollow Metal Frames in the Fire Service Tech and EMT Areas
- Finishing of Drywall in the Exercise Science and Dental Assisting Labs
- Prime and First Coat of Paint in Cosmetology
- Installation of Acoustical Ceiling Grid in Cosmetology

Requests for Information

- RFI's to Date: 362
- Open RFI's: 3
- Urgent: 0



Picture 2: Finishing of Drywall in the Manicure Room

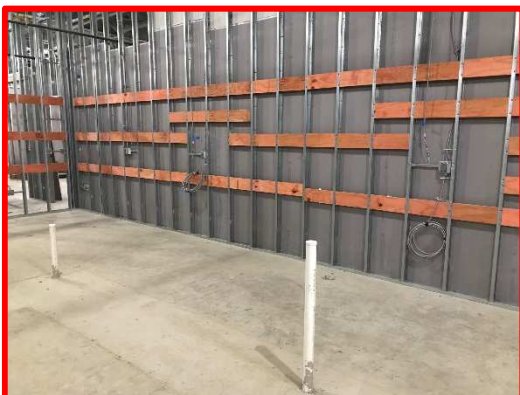

Picture 3: In-Wall Blocking and Electrical Rough-In in the Chemistry Lab

WEEKLY SUMMARY

November 2, 2018



Picture 4: Staging of Material for Drywall Installation in Area G classrooms



Picture 5: View from Consultation Room into the Exercise Science Lab



Picture 6: In-Wall Plumbing Rough-In for Water Fountain in Fire Service Tech
