

20-574
HANOVER
EAST
MOREHEAD

Weekly Site Photos
Week Ending

6/2/2023



ELEVATION VIEW

Northwest Corner

E. Morehead St. and Euclid Ave.

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



ELEVATION VIEW

North Side

Euclid Ave.

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



ELEVATION VIEW

East Side

Royal Ct.

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 16 AMENITY DECK

Topping Slab Formwork

MEP Rough-ins

Fitness Room Framing

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 16 UNITS

Ceiling Prerock

MEP Rough-ins

Window Wall Installation



20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 14 UNITS

MEP Rough-ins

Pre-Cover Inspections Complete

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 12 UNITS

Drywall Hanging

Tape and Float

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 11 UNITS

Prime and First Coat

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 10 UNITS

Interior Framing

MEP Rough-ins

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 9 UNITS

Interior Trim

MEPF Trim Out

Cabinets Delivered

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 8 UNITS

Cabinet Installation

MEPF Trim Out

Corridor Tape and Float

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 7 UNITS

*Countertop and Backsplash
Installation*

Wood Flooring Installation

Corridor Tape and Float

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 6 UNITS

Wood Floors

Permanent Power On

Minor Appliances

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 5 UNITS

Major Appliances

Permanent Power On

Rough Clean Complete

Construction Punch Ongoing

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 4 UNITS

Rough Clean Complete

Construction Punch Ongoing

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 1 TOWNHOMES

Countertop Installation

MEP Trim out

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



LEVEL 1 LEASING

Millwork Deliveries and Installation

Trim Installation

Mailbox Finishes

Elevator Lobby Framing

Bathroom Tile




20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023

GOLF SIMULATOR

Interior Framing

MEP Rough-in

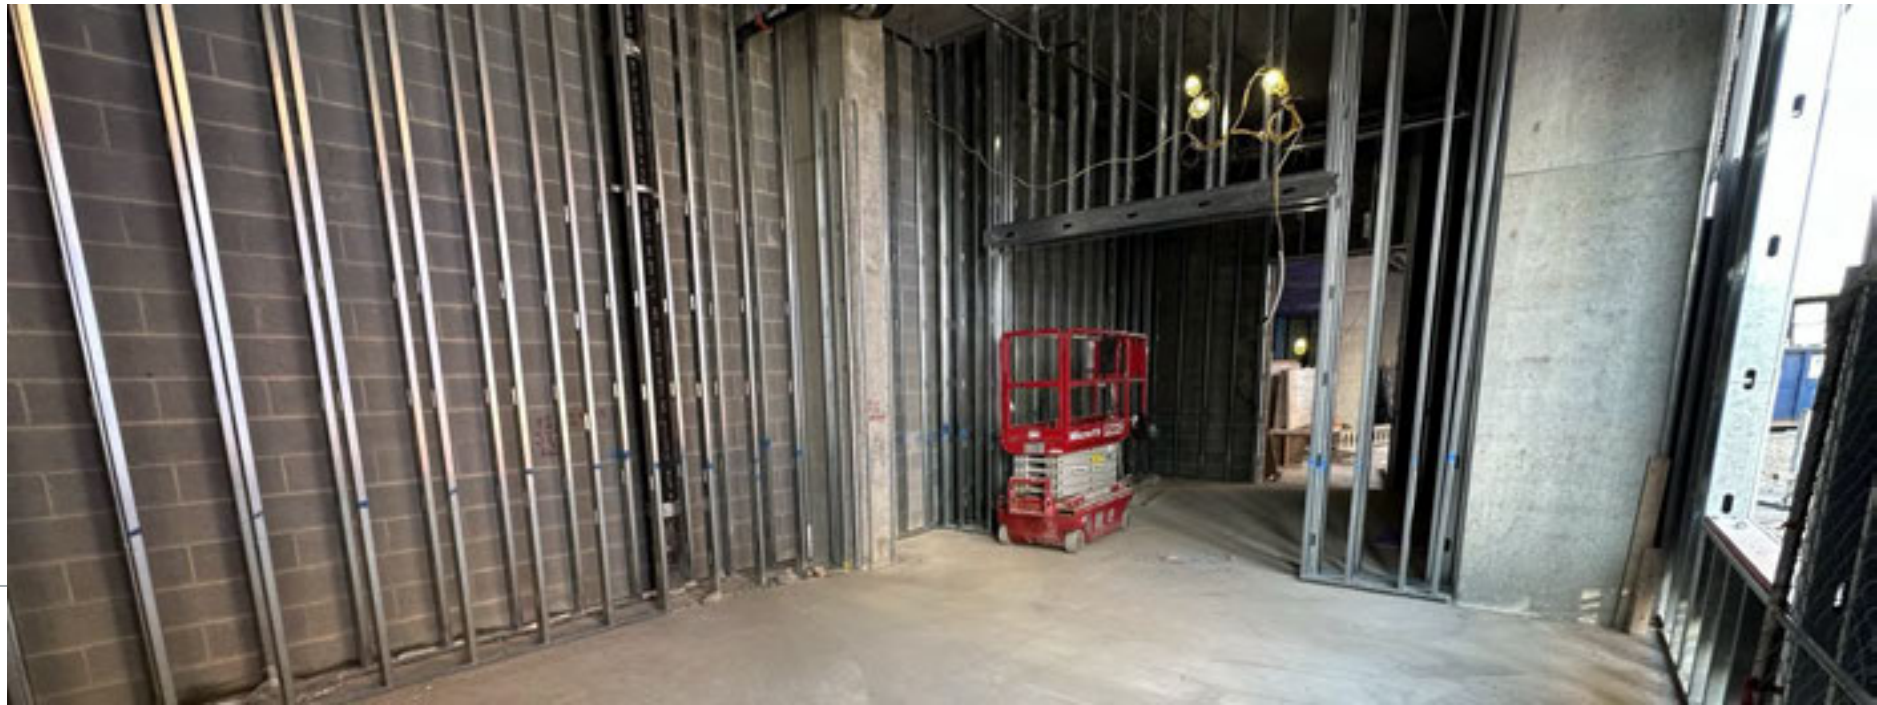

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023

LEVEL 1 MOTORCOURT

Sheathing Installation

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



DOG WASH

Cement Board Installation Complete

Ceiling Sheetrock

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
6/2/2023



HANOVER
