

19-565  
Hanover  
1230 West  
Peachtree

---

Weekly Site Photos  
Week Ending  
9/1/2023





## North-East

*Elastomeric Coating Completed on the East and 90% Complete on the North.*

*Balcony Railing Completed 90%.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023




## South-East

*Elastomeric Coating Completed on the East and 90% Complete on the South.*

*Balcony Railing Completed 90%.*

*Parapet Glazing Installation Complete Along the East Elevation and 95% on the South Elevation.*

**19-565 Hanover 1230 West Peachtree**  
**Weekly Site Photos**  
**Week Ending**  
**9/1/2023**

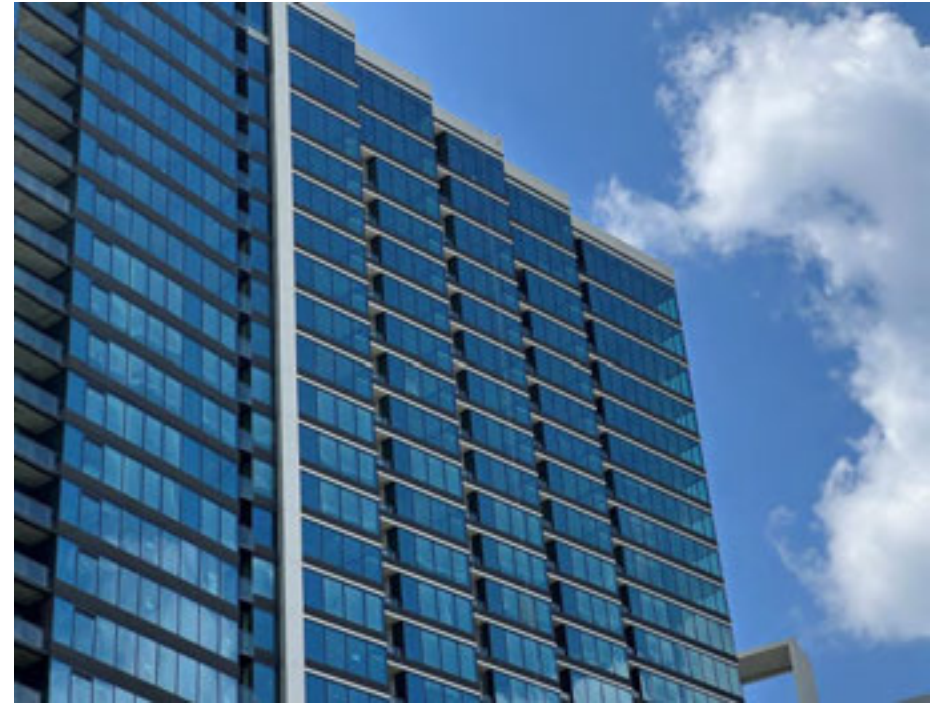



## West Tower

*Elastomeric Coating Completed  
75%.*

*Balcony Paint in Progress.*

19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023





# North

*Elastomeric Coating 90% Complete.*  
*Metal Panel Installed at Level 6 Slab*  
*Edge.*



**19-565 Hanover 1230 West Peachtree**  
**Weekly Site Photos**  
**Week Ending**  
**9/1/2023**



# Amenity Deck

*Metal Panel Installed at Level 6 Slab Edge.*

*Security Fence Installed Along the South Elevation.*

*Wood Plank Tile Installation in Progress.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023

# Clubhouse

*Clubhouse Level 5 Spraying  
Completed.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023





# Leasing Lobby


*Mailbox Installation Complete.*

*Tile Installation at Mail Room.*

*Moz Ceiling Installation in Progress.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023

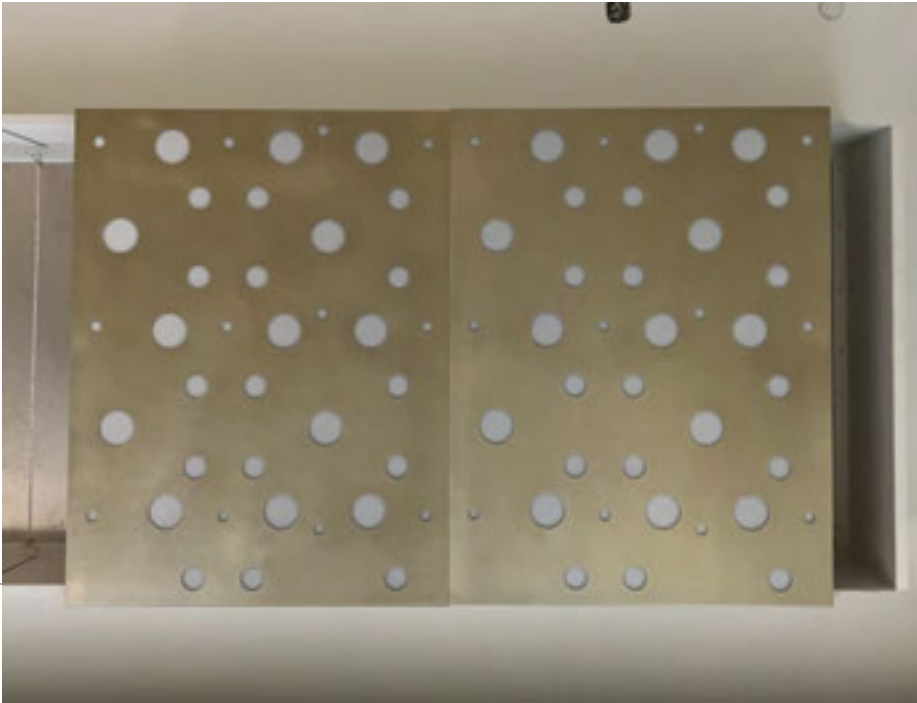



# Motor Court

*Stucco Complete on the North and South Drive.*

*Electrical Trim-out Started.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023





## 15<sup>th</sup> Street Access Road

*Access Road in Progress.*

19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023





## Elevator Lobby

*Level 7-10 Elevator Lobby City  
Inspection Passed.*

19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023





# Roof

*Exterior Glass Framing and  
Glazing Installation Complete Along  
the South and East Elevations.*

*Condenser Disconnect Installation  
Continues.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023



## Level 7

*Permanent Power in Place for Level 7  
to Level 9.*

*Construction Punch in Progress.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023





## Level 10

*Cabinet Installation Complete.*

*MEPF Trim Out Nearing Completion.*

*Shower Door Installation Completed.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023





## Level 14

*Wood Flooring Installation in Progress.*

*Kitchen Backsplash.*

*Plumbing Fixture Installation.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023





## Level 17

*Cabinet Installation in Progress.*

*Bathroom Tile Installation in Progress.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023





## Level 20

*Knee-wall Stool Installation in Progress.*

*Corridor Base and Door Casing Installation in Progress.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023



Level 23

*Final Prep for Painting Complete.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023

**Level 26**

*2-Sided Drywall Hanging Nearing Completion.*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023



## Level 29

*HVAC Rough-in Complete.*

*Corridor Electrical Rough in Started*



19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023






## Level 31

*Unit Wall Framing Complete.*

*Resilient Channel Installation Complete.*

*Unit Pre-Rock Installation in Progress.*

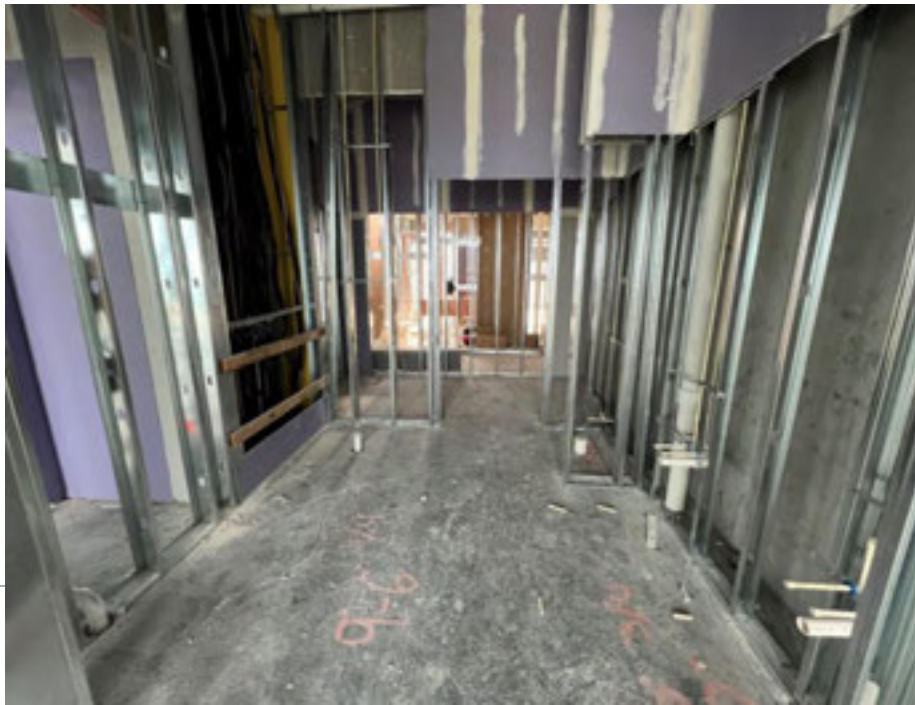

19-565 Hanover 1230 West Peachtree  
Weekly Site Photos  
Week Ending  
9/1/2023



**HANOVER**
