

21-596 Hanover Laguna Niguel

Weekly Site Photos
Week Ending
6/2/2023



Elevation Overviews

Top- View from NW

Bottom Left – View from South

Bottom Right – View from SW

21 – 596 Hanover Laguna Niguel
Weekly Site Photos
Week Ending
6/2/2023



Garage Overview from SW Elevation

21 – 596 Hanover Laguna Niguel
Weekly Site Photos
Week Ending
6/2/2023



Garage – Level 4 to 5

CMU continued on level 6

Perm light Installment began and continued on level 2

Fire Sprinkler continued on level 5

Caulking at CMU initiated

21 – 596 Hanover Laguna Niguel
Weekly Site Photos
Week Ending
6/2/2023



Residential

Overview of Residential Operations


21 – 596 Hanover Laguna Niguel
Weekly Site Photos
Week Ending
6/2/2023



Residential – Area 2B

Pour Complete

21 – 596 Hanover Laguna Niguel
Weekly Site Photos
Week Ending
6/2/2023

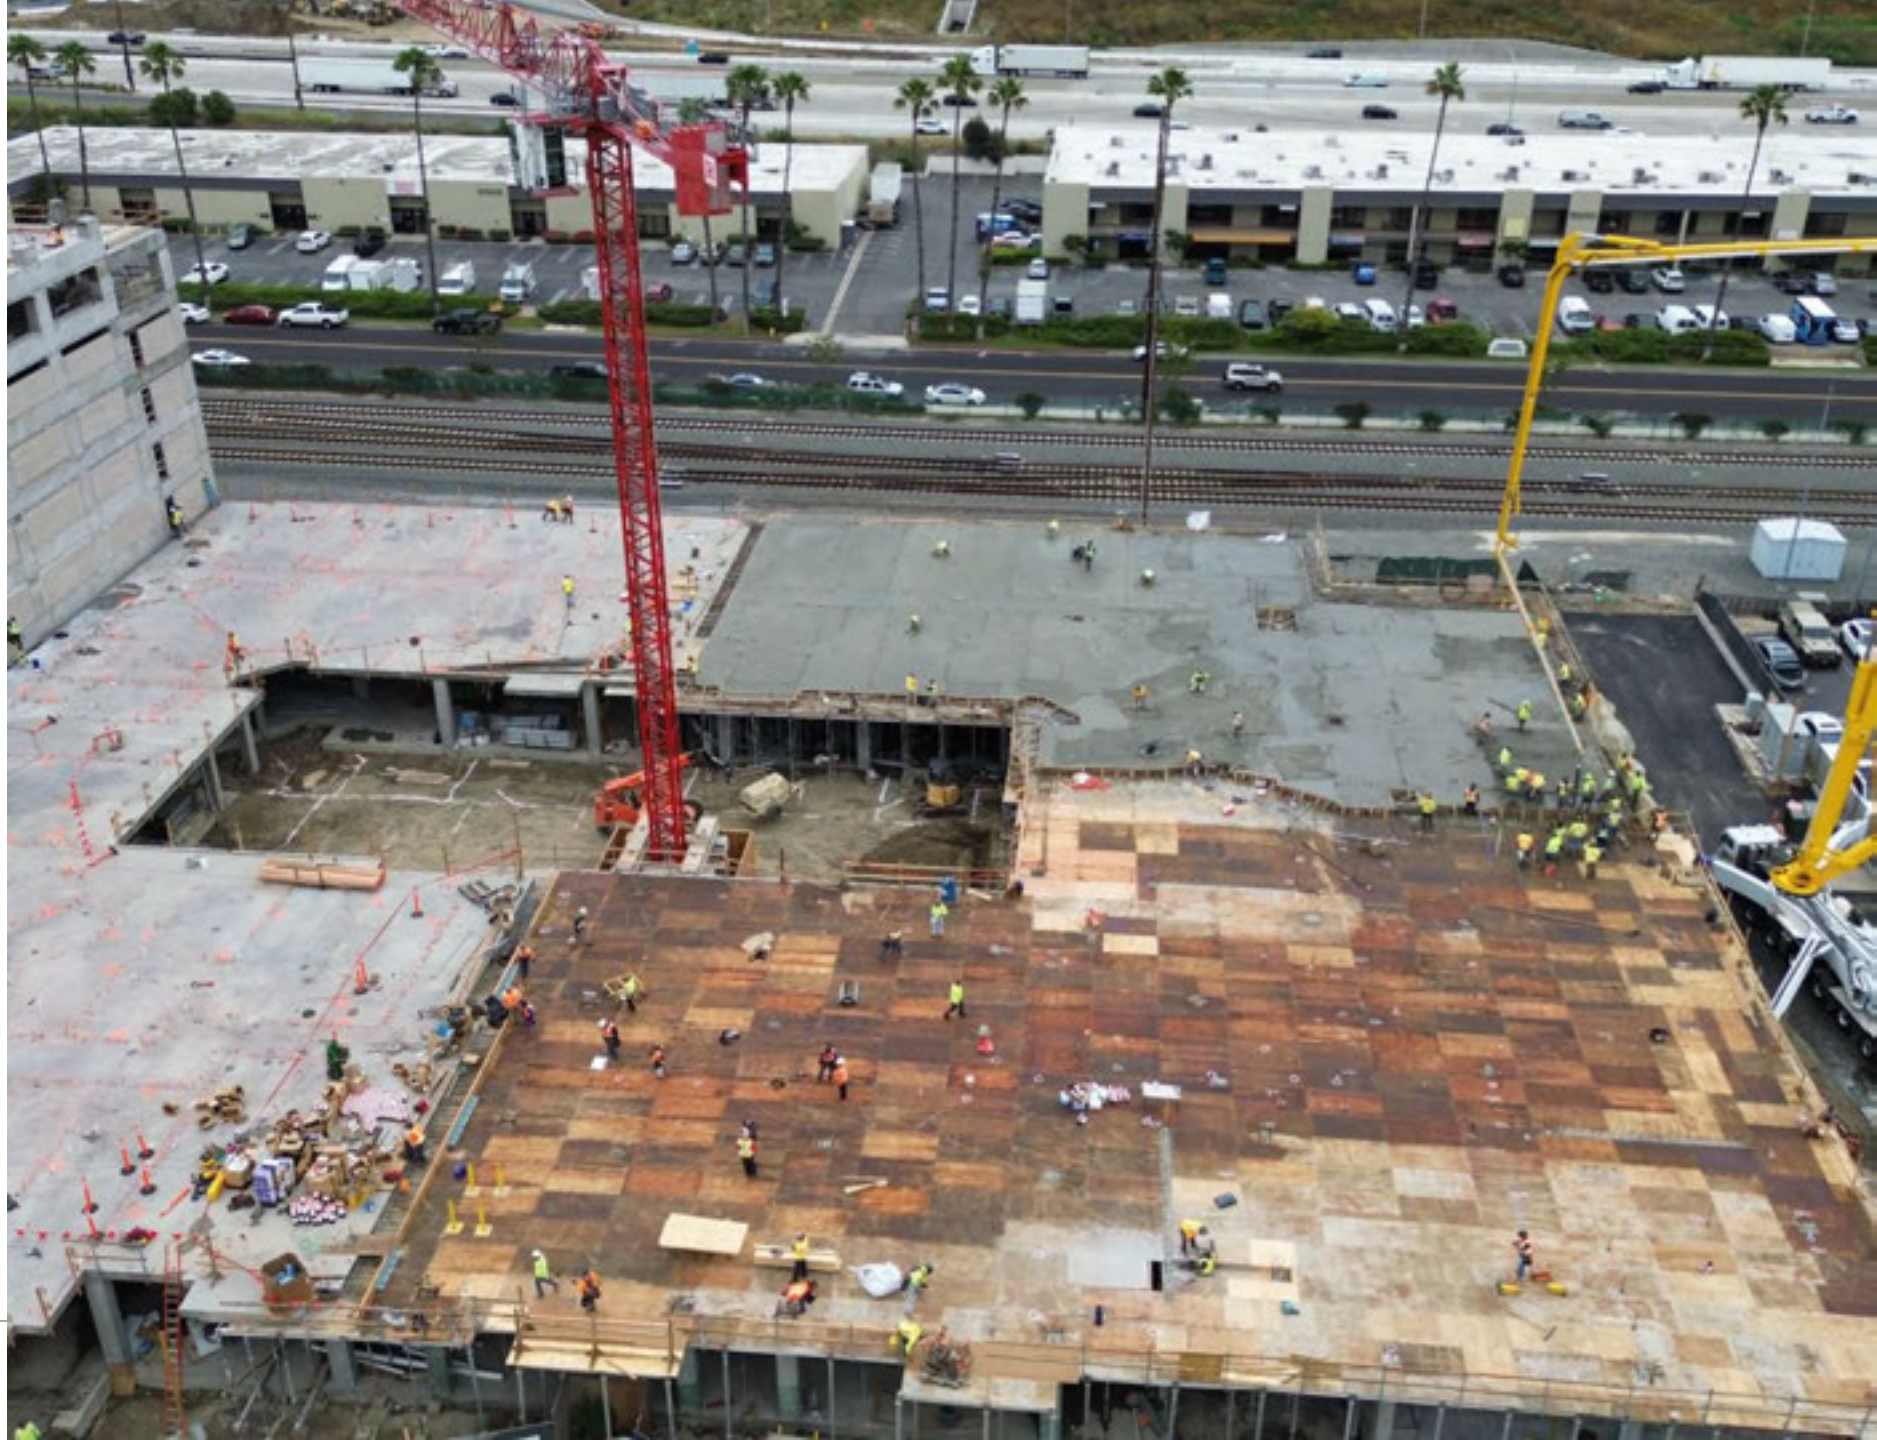

Residential – Area 2A

*Deck and slab edge formwork
complete*

MEP's complete

Rebar to continue

21 – 596 Hanover Laguna Niguel
Weekly Site Photos
Week Ending
6/2/2023



Courtyard

Underground drain line placement at courtyard started, to continue


21 – 596 Hanover Laguna Niguel
Weekly Site Photos
Week Ending
6/2/2023



Concrete Phasing Plan

Reference Sequencing/ callouts for prior slides

21 – 596 Hanover Laguna Niguel
Weekly Site Photos
Week Ending
6/2/2023

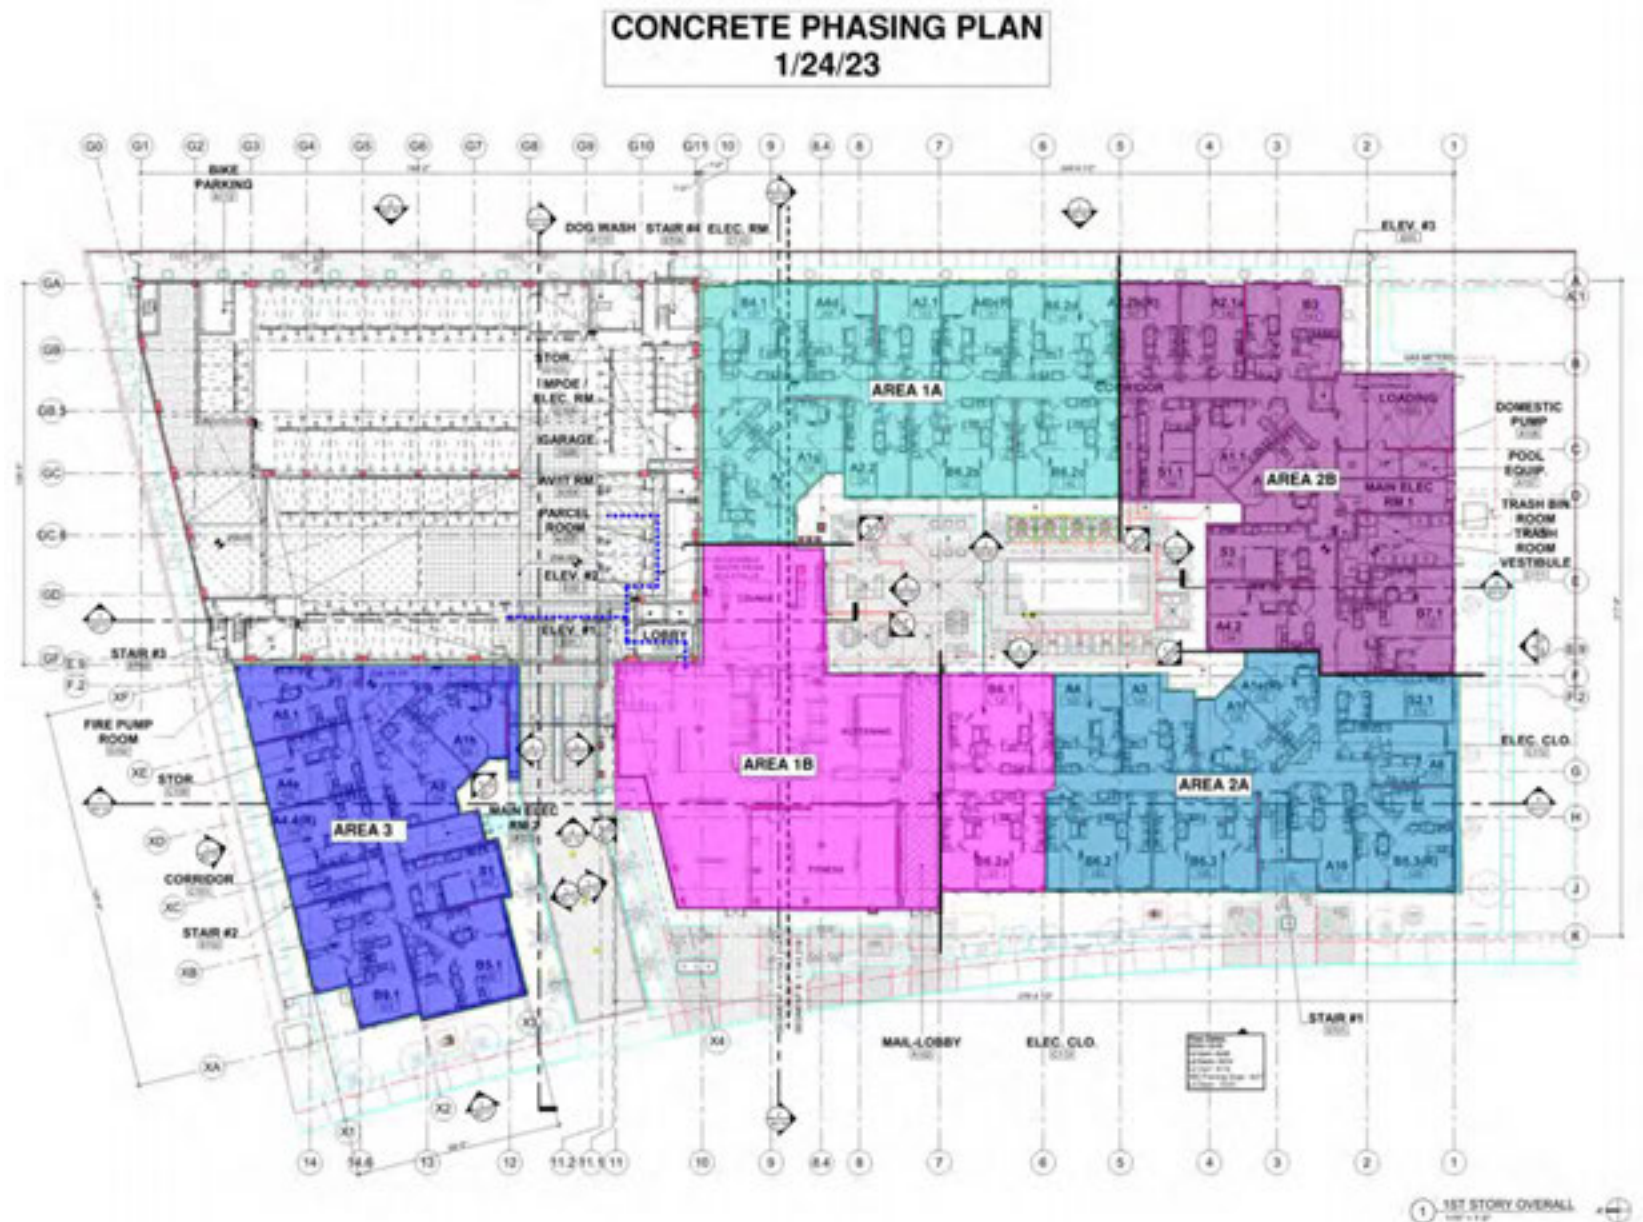

HANOVER
