



Hanover East Morehead – Weekly Photos

Week Ending 03.24.2023

Week of 03/24/2023 Elevation View



Photo Date: 03/24/2023

Location: Northwest Corner (E. Morehead & Euclid Ave.)

Week of 03/24/2023 Elevation View



Photo Date: 03/24/2023
Location: Northeast Corner (Royal Ct. & Euclid Ave.)

Week of 03/24/2023 Elevation View



Photo Date: 03/24/2023
Location: Southeast Corner (Royal Ct.)

Week of 03/24/2023

Exterior Skin



Photo Date: 03/24/2023
Location: Level 4 Courtyard (West)
Description: Brick installation is ongoing. (Level 11-15)

Week of 03/24/2023

Exterior Skin



Photo Date: 03/24/2023
Location: West Elevation From HydroMobile (Level 15)
Description: Brick installation is ongoing. (Level 15-16)

Week of 03/24/2023

Exterior Skin



Photo Date: 03/24/2023
Location: Penthouses West Side
Description: Window Wall installation is ongoing.

Week of 03/24/2023

Exterior Skin



Photo Date: 03/24/2023

Location: North Elevation

Description: Brick installation is ongoing. Level 15 complete.

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023

Location: Level 15 Units

Description: Interior Framing is ongoing. (Level 15-16)

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023
Location: Level 12 Units
Description: MEP Rough in is ongoing. (Levels 11-14)

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023
Location: Level 10 Units
Description: Unit Interior framing is ongoing. (Levels 10)

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023
Location: Level 9 Units
Description: MEP Inspections are ongoing.

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023
Location: Level 8 Units
Description: Drywall is ongoing.

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023
Location: Level 7 Units
Description: Trim Installation is nearing completion

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023
Location: Level 7 Units
Description: Bathroom Tile install nearing completion.

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023
Location: Level 6 Units
Description: Cabinets installation is ongoing

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023
Location: Level 6 Corridor
Description: Corridor Wall Priming is ongoing.

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023

Location: Level 5 Units

Description: Wood Flooring, Cabinet, and Backsplash installation is ongoing.

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023

Location: Level 4 Units

Description: Major Appliance Deliveries ongoing. MEPF Trimout is ongoing.

Week of 03/24/2023

Unit Interiors



Photo Date: 03/24/2023
Location: Townhome Units
Description: Trim Installation is ongoing.

Week of 03/24/2023 Amenities



Photo Date: 03/24/2023

Location: Level 1 Mail Room

Description: Mailbox Bottom Track installation is complete.

Week of 03/24/2023

Amenities



Photo Date: 03/24/2023
Location: Level 16 Pool Deck
Description: Pool Deck Prep is ongoing.

Week of 03/24/2023

Motor Court

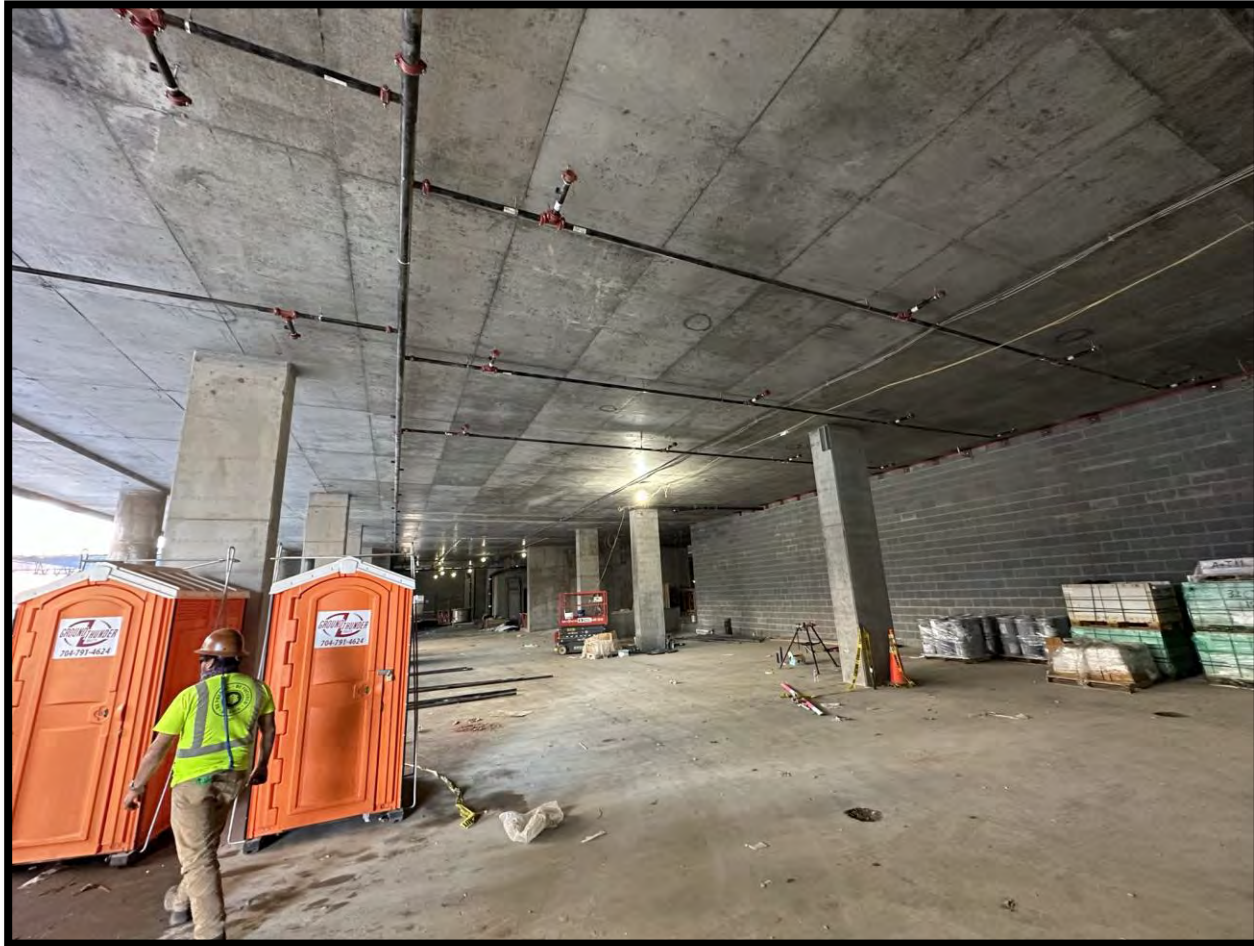


Photo Date: 03/24/2023
Location: Level 1 Motor Court
Description: Fire Sprinkler Installation is ongoing.
