

21 – 615

HANOVER RIVERWALK

Weekly Site Photos
Week Ending

5/19/2023



Elevation Progress

*View from Southeast Corner at
Grade Level.*

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



PC-B Pour Prep

*Malcolm Drilling – Chipping Piles down to elevation. Tower side.
(Ongoing)*

KD Construction – Building forms around PC-B. Tower side. (Ongoing)

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



PC-B Pour Prep

*KD Construction – Laying down gravel, rebar, while building forms around PC-B. Tower side.
(Ongoing)*



21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023

PC-B Pour Prep

*KD Construction – Formwork
completed and currently laying down
rebar. Tower side.
(Ongoing)*

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Garage Crane Erection

KD Construction – Laying down gravel for PC-D preparing for formwork and rebar. Garage Crane. (Ongoing)

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Garage Crane Erection

*KD Construction – Starting to lay down rebar for PC-D. Garage Crane.
(Ongoing)*


21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Garage Crane Erection

KD Construction – Starting to lay down rebar and formwork for PC-D. Garage Crane. (Ongoing)

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023

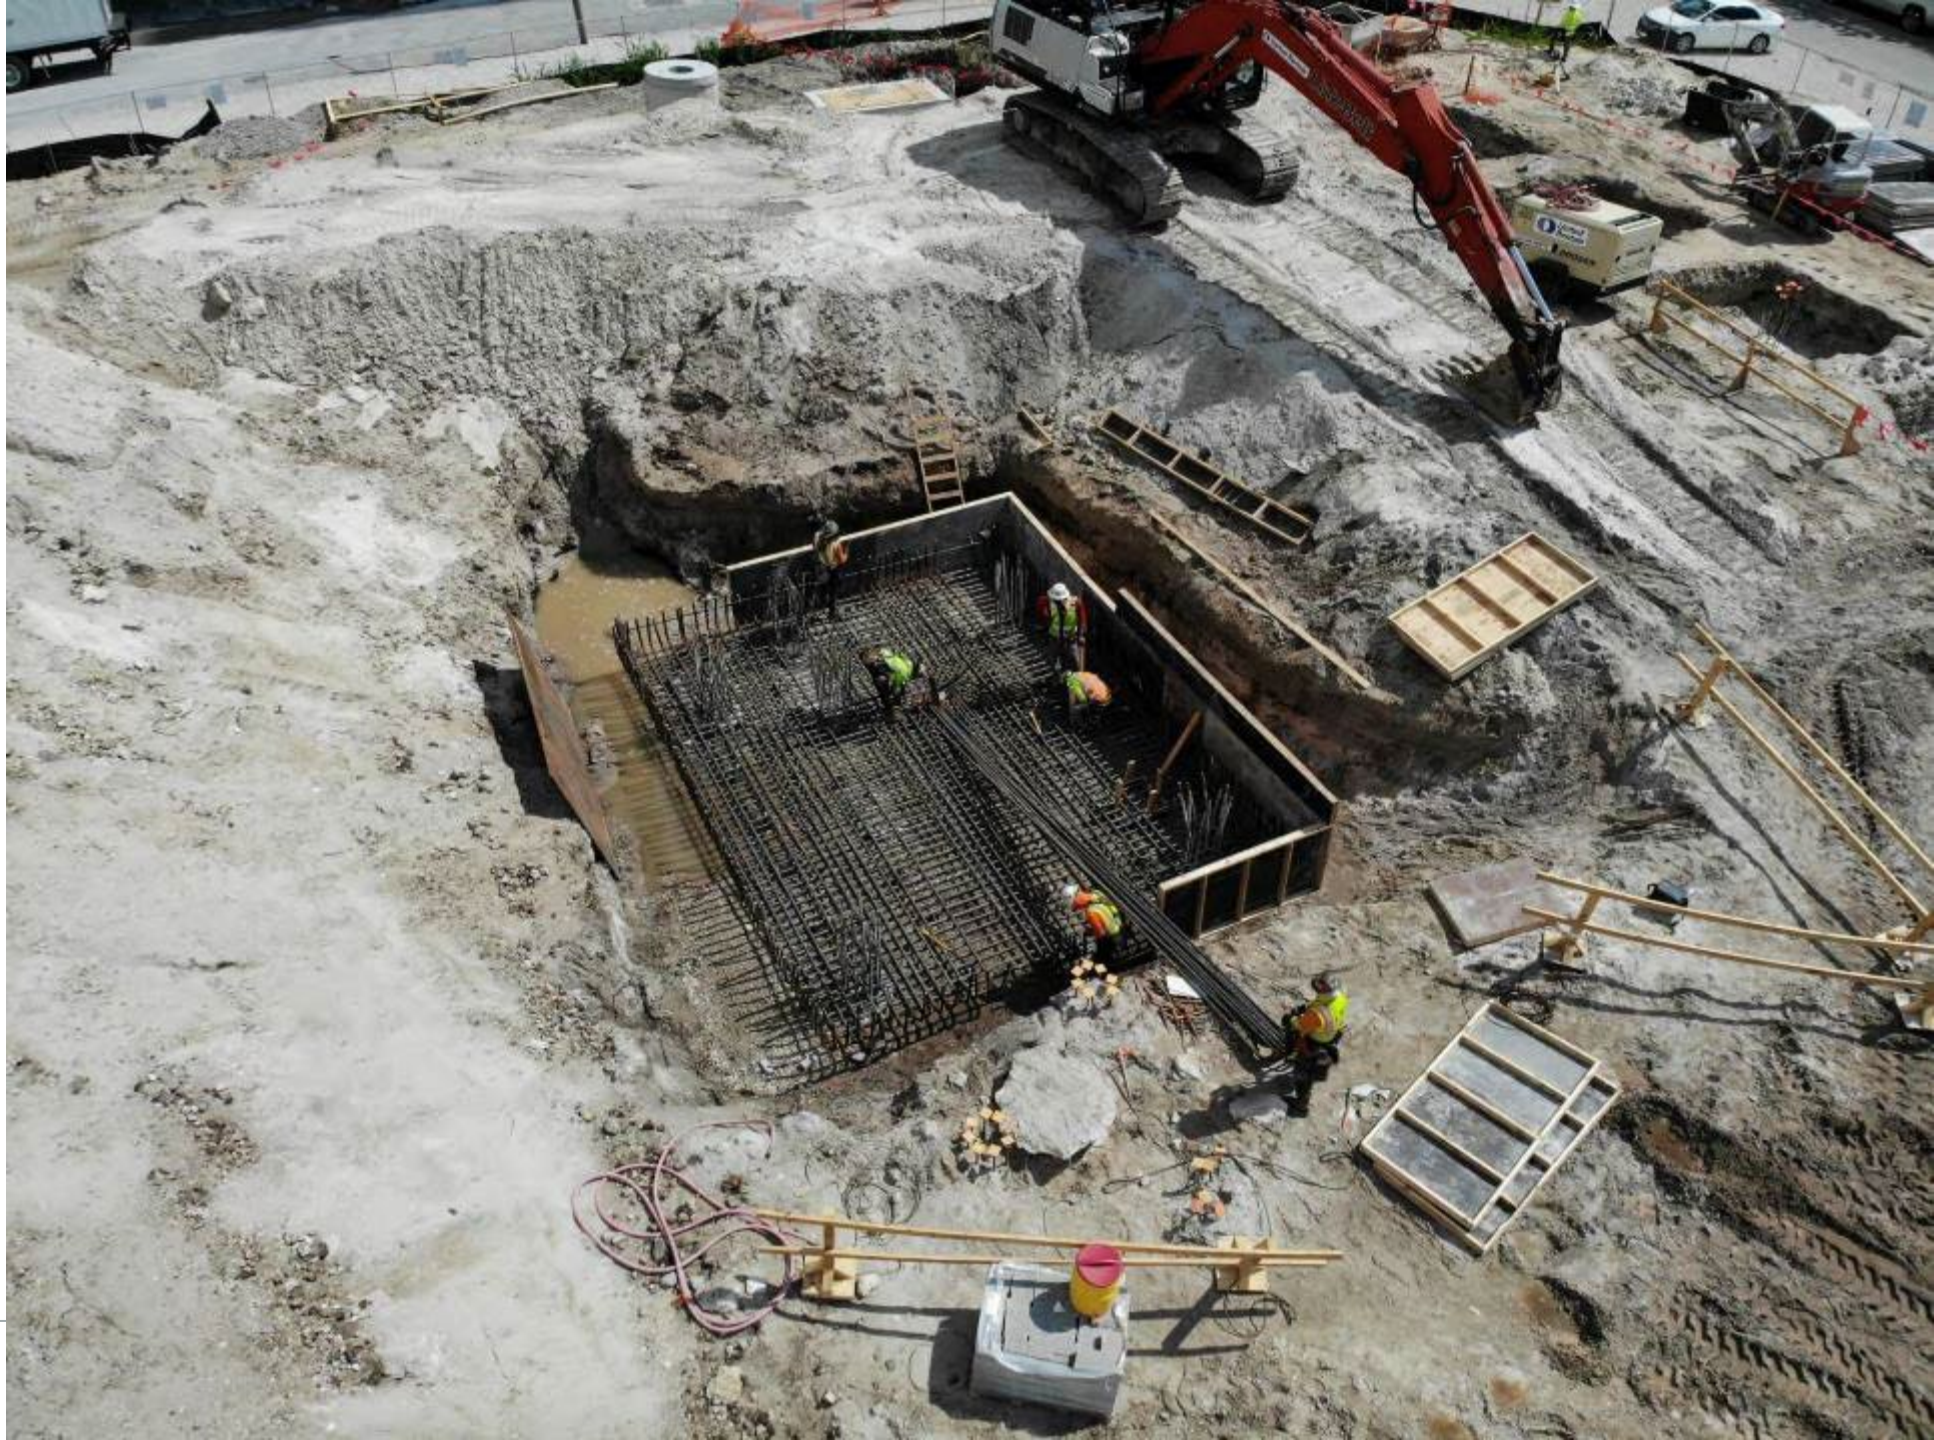

Pile Caps

*Malcolm Drilling – Chipping Piles
down to elevation. Garage side.
(Ongoing)*

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Tower Crane Erection

*KD Construction – Concrete pour for
PC-C completed. Tower Crane.*

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Tower Crane Erection

*KD Construction – Backfilling dirt
around completed PC-C. Tower
Crane.*

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Tower Crane Erection

*KD Construction – Completed PC-C
for further erections. Tower Crane.*

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Tower Crane Power

Vankirk Electric – Installed and completed power disconnect box for Tower Crane.

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Dewatering

*Florida Civil – Dewatering System
actively pumping water off site.
(Ongoing)*



21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023

Aerial Photo

Southeast

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Aerial Photo

South

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Aerial Photo

Southwest

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Aerial Photo

West

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Aerial Photo

Northwest

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Aerial Photo

North

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Aerial Photo

Northeast

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



Aerial Photo

East

21-615 Hanover Riverwalk
Weekly Site Photos
Week Ending
5/19/2023



HANOVER
