

20-574
HANOVER
EAST
MOREHEAD

Weekly Site Photos
Week Ending
9/1/2023



ELEVATION VIEW

Northwest Corner

E. Morehead St. and Euclid Ave.

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



ELEVATION VIEW

North Side

Euclid Ave.

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



ELEVATION VIEW

East Side

Royal Ct.

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 16 CLUBHOUSE


Top – Fitness Room MEP Roughing

Bottom Left - Pantry Framing

*Bottom Right – Screening Room
Framing*



20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023

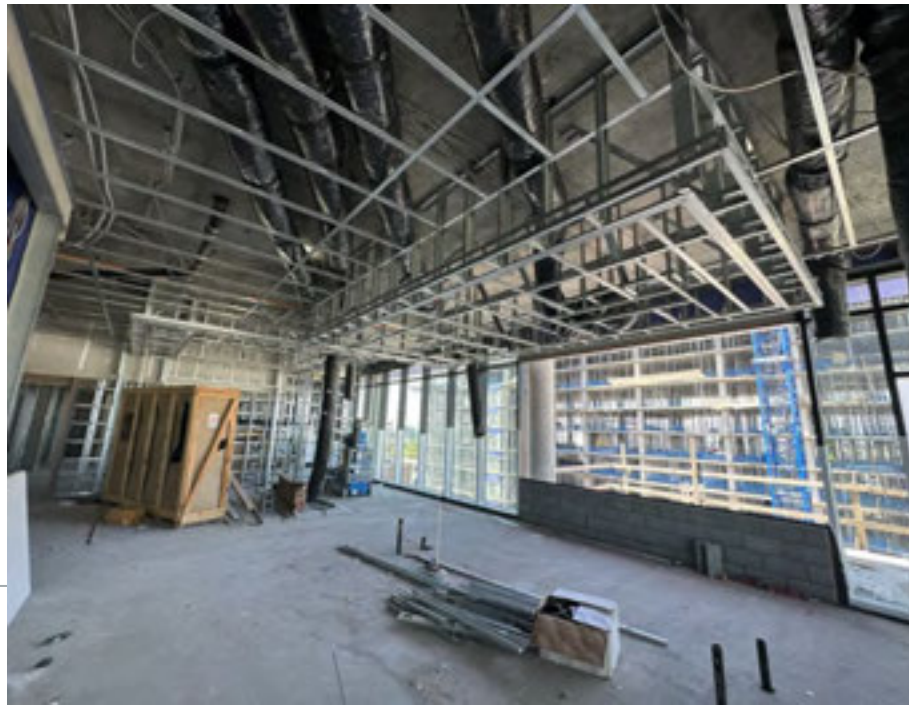

LEVEL 16 POOL DECK

Pool Soffit Sheathing

MEP Rough-ins and Inspections



20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 16 UNITS

MEP Rough-ins

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 15 UNITS

Sheetrock

Tape and Float

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 14 UNITS

Interior Door and Trim Installation

MEP Trim Out

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 12 UNITS

Cabinet Deliveries

MEP Trim Out

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 11 UNITS

Cabinet Installation

Countertop Installatoin

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 10 UNITS

Door and Trim Paint

Bathroom Tile

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 9 UNITS

Wood Flooring Installation

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 8 UNITS

Rough Clean

Construction Punch

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 7 UNITS

Carpet Installation

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 6 UNITS

Final Paint Ongoing

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 5 UNITS

Permanent Door Hardware Install

Bathroom Mirror Install




20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023

LEVEL 4 COURTYARD

First Course of CMU

Topping Slab Prep

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023

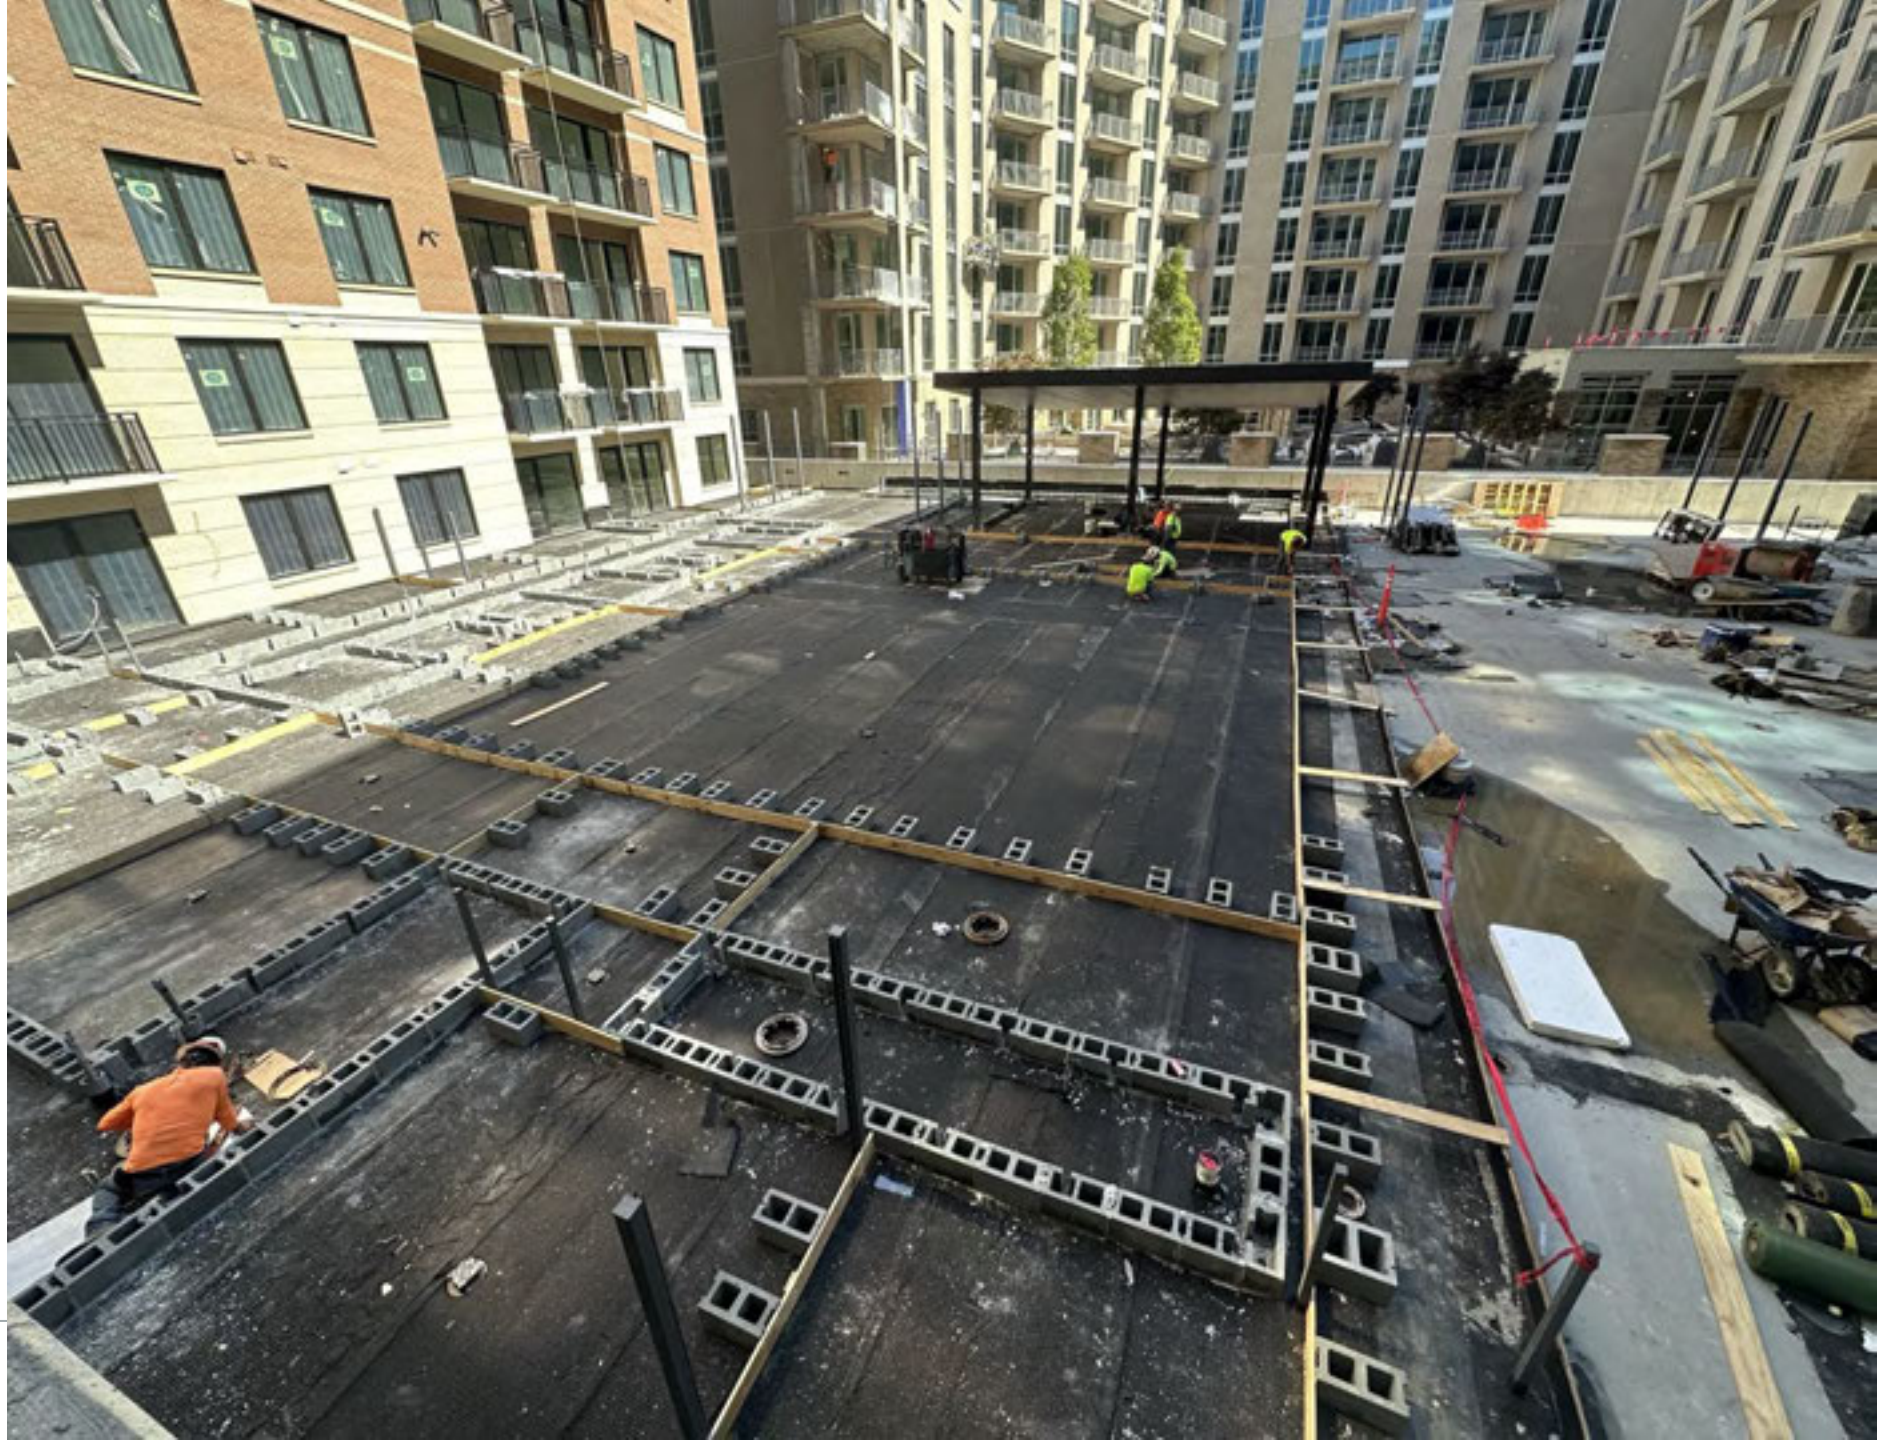

LEVEL 1 TOWNHOMES

Appliances Delivered

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



LEVEL 1 LEASING

Elevator Lobby Floor Tile

Concierge Large Format Tile



20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



GOLF SIMULATOR

Prime and First Coat Ongoing

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



Motor Court

Stucco Ongoing

20-574 Hanover East Morehead
Weekly Site Photos
Week Ending
9/1/2023



HANOVER
