

21-592 Hanover Edgewood

Weekly Site Photos
Week Ending
9/1/2023



Phase 1 & 2 Overview

21-592 HANOVER EDGEWOOD
Weekly Site Photos
Week Ending
9/1/2023



Phase 3 & 4 Overview

21-592 HANOVER EDGEWOOD
Weekly Site Photos
Week Ending
9/1/2023



Exterior Mockup

*Hanover Design was on site, 8/30,
to review the exterior building
mockup.*

21-592 HANOVER EDGEWOOD
Weekly Site Photos
Week Ending
9/1/2023



Phase 1 – Exterior Progress

Continued installing Tyvek on the West and East elevations for phase 1.

Window Installation in progress



21-592 HANOVER EDGEWOOD
Weekly Site Photos
Week Ending
9/1/2023

Phase 1 – Below Podium Progress

Installing Temp FDC in pump room.

Continued installing pre-rock in the wet areas and installed blocking for tubs and showers.

Started running overhead MEPs through the furr downs in the below podium units.



21-592 HANOVER EDGEWOOD
Weekly Site Photos
Week Ending
9/1/2023

Phase 1 – Above Podium Progress

Finished framing out units for phase 1 level 8.

Started installing roof trusses.

Continued applying mold spray throughout the corridors for phase 1 levels 6 & 7.

Continued working on MEP activities for phase 1 levels 5 & 6



21-592 HANOVER EDGEWOOD
Weekly Site Photos
Week Ending
9/1/2023

Phase 2 – Exterior Progress

Installing exterior sheathing on the South and West elevations on phase 2



21-592 HANOVER EDGEWOOD
Weekly Site Photos
Week Ending
9/1/2023



Phase 2 – Above Podium Progress

Completed unit framing for phase 2 levels 7 & 8.

Continued framing out units for phase 2 level 4

Started installing decking for phase 2 level 5.

Layout for phase 2 level 5.




21-592 HANOVER EDGEWOOD
Weekly Site Photos
Week Ending
9/1/2023

Phase 4 - Progress

Finished installing vapor barrier for phase 4 level 1.

Poured concrete for phase 4 level 1 slab on Thursday, 8/31.

Started installing deck shoring for phase 4 level 2 deck.

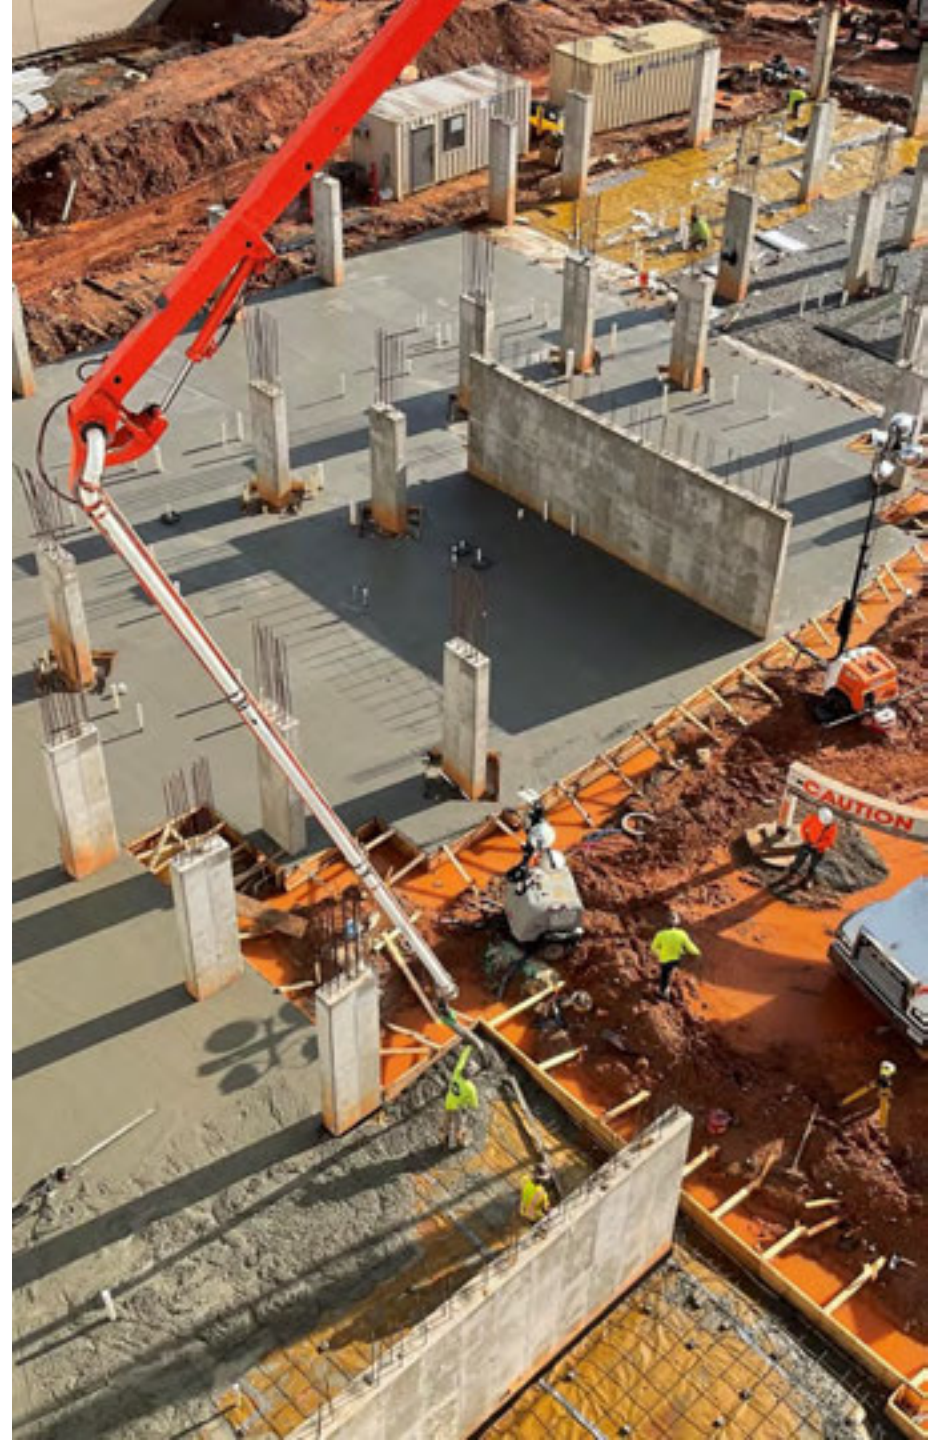

21-592 HANOVER EDGEWOOD
Weekly Site Photos
Week Ending
9/1/2023

HANOVER
