

### TIMELINE

March 15

Excavation for  
Addition

*\*Timeline dependent  
on soil conditions*

Week of March 26

Construction of  
Addition  
Exterior Walls

October 2018

Anticipated end date  
of construction



### Questions?

Email Paul Boening  
Village Manager:


[p.boening@wfbvillage.org](mailto:p.boening@wfbvillage.org)



## Village Hall Building Project Construction

The Village Hall Building Project has now been underway for four months and remains on schedule for completion in October 2018.

As 2017 drew to a close, asbestos abatement was completed, allowing the new year to begin with the continuation of interior demolition and renovation. In February, one of the facility's existing elevators was removed due to age and the area received new flooring to accommodate office space. The remaining elevator will go through a modernization process. Framing of new walls was also completed throughout the building. As the project progressed into March, construction of the masonry walls in the new detention area and utility relocation were completed.

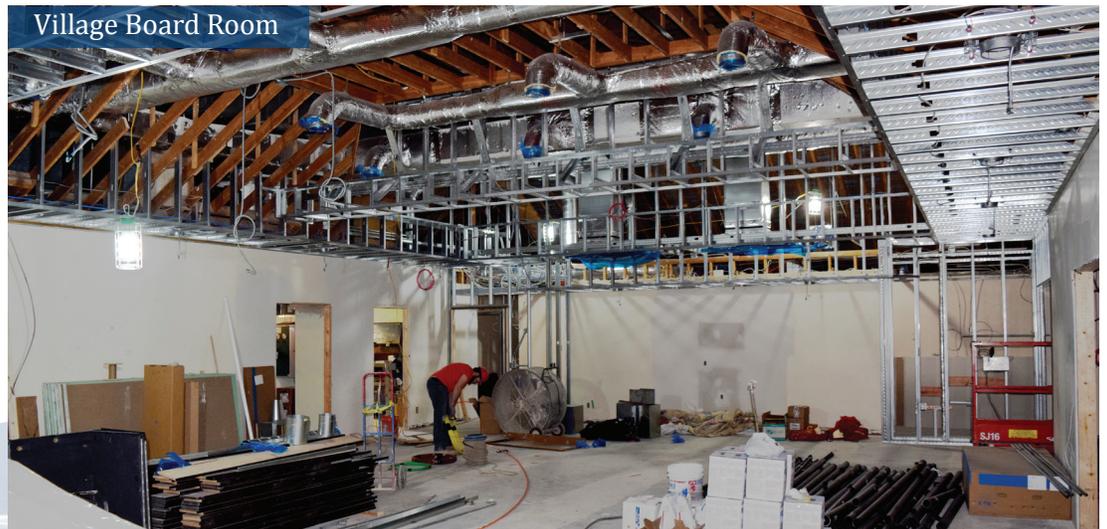

### CONSTRUCTION NEXT STEPS

Scherrer Construction will begin exterior excavation for the police garage addition the week of March 12 (*timeline is dependent on soil conditions*); this will include the creation of new footings and foundations, removal of an aging diesel tank, and parking lot demolition. Roofing is slated to begin in mid-April and asphalt paving in late May.

Within the building, sprinkler system piping installation is ongoing. Drywalling will begin following an inspection on March 20. Through April and into May, the building will be insulated, the brick facade will be laid, and windows and doors will be installed.
