

## CITY OF GILROY

## FY24 CITYWIDE PAVEMENT REHABILITATION PROJECT SLURRY SEAL SCHEDULE


MONDAY 8/26/24		
STREET	FROM	TO
MANTELLI DR (split outside / inside)	WEST END	COUNTRY DR
STEWART CT	AYER DR	END
BLAKE CT	END	SANTA THERESA DR
SANTA THERESA DR	PERRELLI ST	W 6TH ST
FOWLER ST	HOXETT ST	WENTZ DR
HOXETT ST	CHADWICK	FOWLER ST
TENTH ST (OUTSIDE)	ALEXANDER ST	540' E/O ALEXANDER ST
TUESDAY 8/27/24		
STREET	FROM	TO
TOYON CT	CUL DE SAC	BAY TREE DR
BAY TREE DR	POPLAR DR	EAST END
MANTELLI DR (split outside / inside)	COUNTRY DR	RANCHO HILLS DR
WILD IRIS DR	MANTELLI DR	SOUTH OF ROUNDABOUT
COLONY CT	RANCHO HILLS DR	END
COLONY WY	END	RANCHO HILLS DR
CRAWFORD CT	CRAWFORD DR	END
THAYER CT	CRAWFORD DR	CUL DE SAC
CARR PL	END	SIXTH ST
WEDNESDAY 8/28/24		
STREET	FROM	TO
LONGMEADOW DR	SANTA TERESA BLVD	HIRASAKI DR
WREN AVE (outside / inside)	FARRELL AVE	VICKERY LN
BRITTANY CT	MANTELLI DR	END
SPENCER CT	MANTELLI DR	CUL DE SAC
SAN MIGUEL ST	SANTA MARIA CT	LOS PADRES CT
HERSMAN DR	SANTA BARBARA DR	STEWART DR
STEWART DR	HERSMAN DR	AYER DR
ARROYO CIR (split)	CAMINO ARROYO DR (north)	GILROY SCHOOL DIST OFFICE
THURSDAY 8/29/24		
STREET	FROM	TO
POPLAR DR	MANTELLI DR	BAY TREE DR
SYCAMORE CT	POPLAR DR	CUL DE SAC
WILLOW CT	POPLAR DR	CUL DE SAC
ELM ST	FOREST ST	SPRINGDALE CT
SPRINGDALE ST	ELM ST	SOUTH CUL DE SAC
ARROYO CIR (split)	GILROY SCHOOL DIST OFFICE	KAISER (SOUTH ENTRANCE)
LOS PADRES CT	SAN MIGUEL ST	END
SAN MIGUEL ST	SANTA BARBARA DR	SANTA MARIA CT
TENTH ST (INSIDE)	ALEXANDER ST	540' E/O ALEXANDER ST
FRIDAY 8/30/24		
STREET	FROM	TO
WREN AVE (outside / inside)	125' S/O WELBURN AVE	FIRST ST
WREN AVE	3RD ST	SIXTH ST
HAGEN CT	WENTZ DR	END
WENTZ DR	WREN AVE	CARR PL
TUESDAY 9/3/24		
STREET	FROM	TO
LONGMEADOW DR	RANCHO HILLS DR	TRAILBLAZER WAY
WELBURN AVE	KERN AVE	PARISH WAY
WREN AVE	FIRST ST	3RD ST
SANTA THERESA DR	3RD ST	PERRELLI ST
WEDNESDAY 9/4/24		
STREET	FROM	TO
CARRIAGE DR	END	RANCHO HILLS DR
LONGMEADOW DR	TRAILBLAZER	CALLE DEL REY
WELBURN AVE	PARISH WAY	WREN AVE
ARROYO CIR (split)	KAISER (SOUTH ENTRANCE)	CAMINO ARROYO (south)
IVY ST	FOREST ST	SPRINGDALE CT
SPRINGDALE ST	NORTH CUL DE SAC	ELM ST





# FY24 CITYWIDE PAVEMENT REHABILITATION PROJECT

## SLURRY SEAL SCHEDULE - SOUTH OF MANTELLI DR

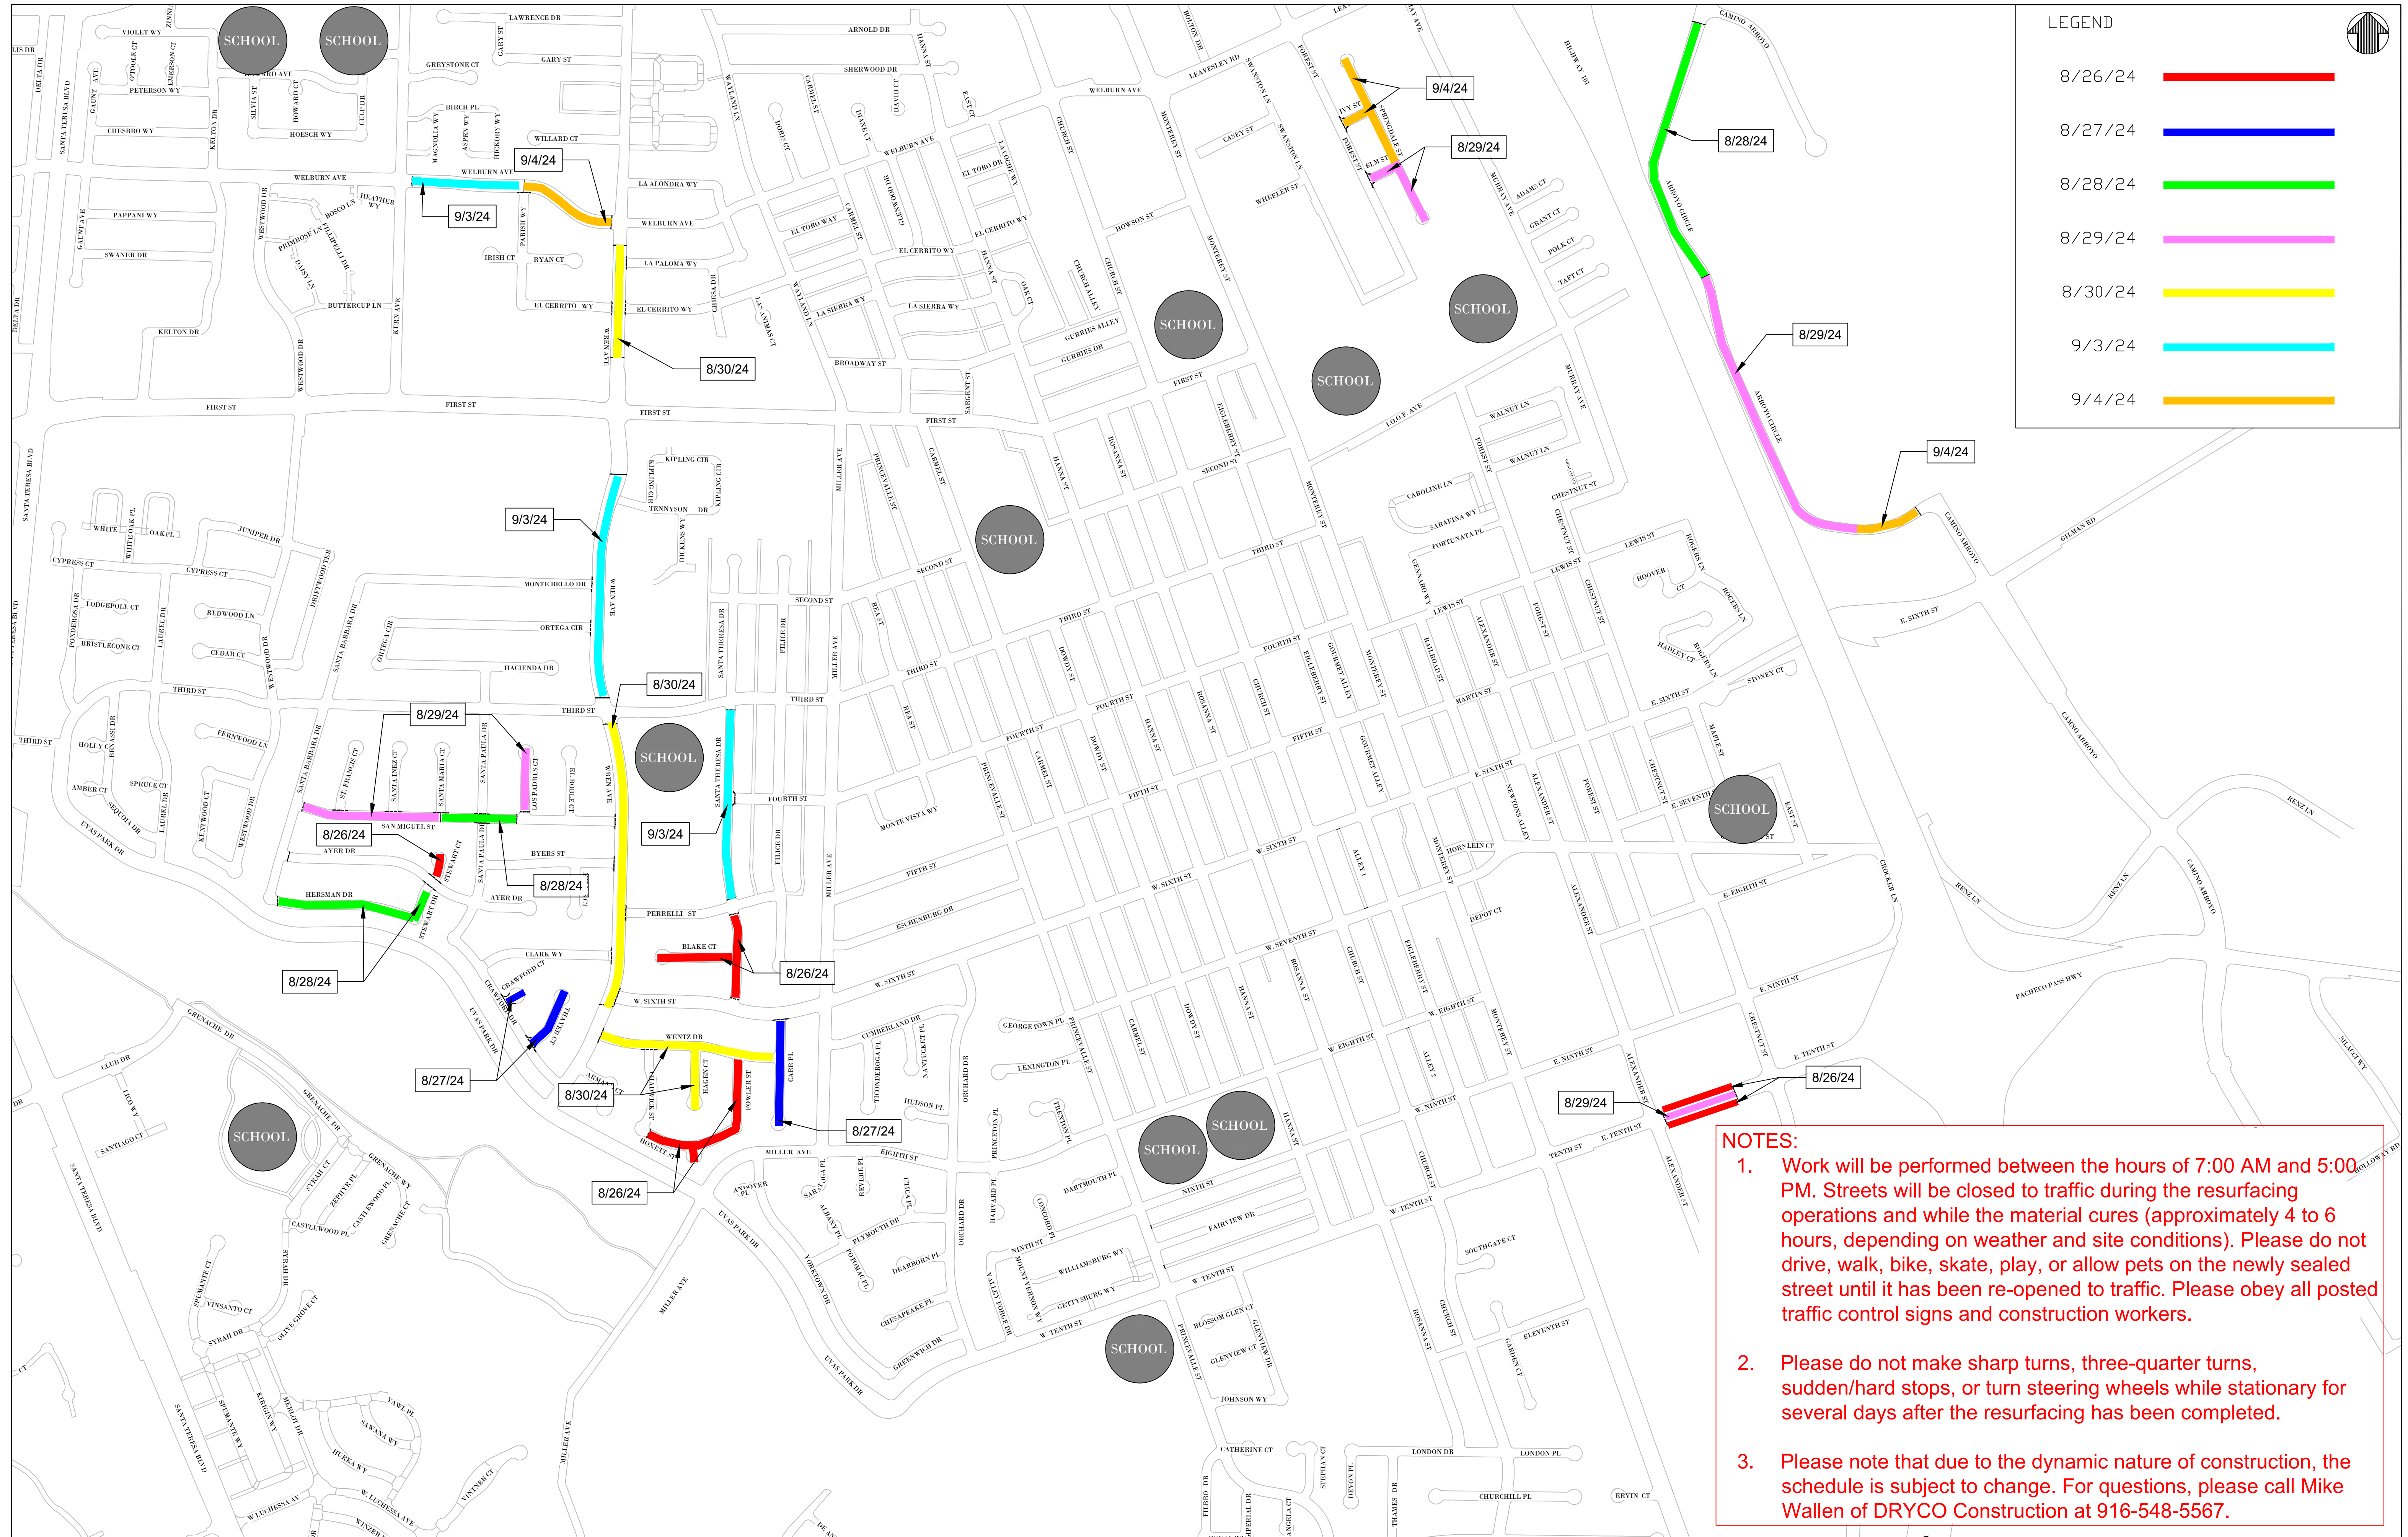

LEGEND

8/26/24	
8/27/24	
8/28/24	
8/29/24	
8/30/24	
9/3/24	
9/4/24	

**NOTES:**

1. Work will be performed between the hours of 7:00 AM and 5:00 PM. Streets will be closed to traffic during the resurfacing operations and while the material cures (approximately 4 to 6 hours, depending on weather and site conditions). Please do not drive, walk, bike, skate, play, or allow pets on the newly sealed street until it has been re-opened to traffic. Please obey all posted traffic control signs and construction workers.
2. Please do not make sharp turns, three-quarter turns, sudden/hard stops, or turn steering wheels while stationary for several days after the resurfacing has been completed.
3. Please note that due to the dynamic nature of construction, the schedule is subject to change. For questions, please call Mike Wallen of DRYCO Construction at 916-548-5567.
