

Airport Bulletin # 22 - 06

Spent Aircraft Deicing Fluid Collection System Reconstruction Project - Final Two Phases

On Monday, March 14, 2022 at 7:00 am, the Airport will commence the Spent Aircraft Deicing Fluid Collection System Reconstruction Project, Final Two Phases. We expect the second phase of this project to be fully completed by Friday, August 26, 2022. Throughout this time period, construction work crews and heavy equipment will be operating Monday thru Friday, between the hours of 7:00 am to 3:30 pm and inside of the orange and white low profile barricades that are flagged, lighted and physically outline the construction phase areas. Details and overhead image of phasing are as follows:


PHASE I - Beginning on Monday, March 14, 2022 and Ending on Friday, May 27, 2022

- Taxiway Alpha between and including Taxiway Delta and Taxiway Echo will remain closed to aircraft movements for construction site work involving the demolition and removal of the existing asphalt pavement, turf shoulders, sub-base material, taxiway lighting and signage and the excavation of old piping and storm water structures. Re-construction includes the installation of sub-base materials, piping, storm water structures, taxiway lighting and signage and new asphalt with pavement markings.
- **Taxiway Alpha east of the construction area will remain open for vehicles, mobile fuel trucks and emergency service apparatus.**
- The Equipment Staging & Materials Area is located at Building #10 Maintenance and will provide for all access to and from the construction site. Taxiway Alpha between the Zulu Tie-down and the active construction area will function as the primary Haul Route for work crews, construction vehicles, equipment and materials.

PHASE II - Beginning on Tuesday, May 31, 2022 and Ending on Friday, August 26, 2022

- Taxiway Alpha between and including Taxiway Charlie and Taxiway Delta will remain closed to aircraft movements for same construction activities as listed above in Phase I. Also, Runway 16/34 will be closed during times when heavy equipment is scheduled to operate in close proximity to Runway 16/34, and will only be closed between the hours from Midnight to 5:30 am.
- **Taxiway Alpha east of the construction area will remain open for vehicles, mobile fuel trucks and emergency service apparatus.**
- At the end of Phase II, Taxiways Alpha, Charlie and Delta will reopen in their new configuration with associated pavement markings, and a new non-movement area vehicle lane will be established between the Hangar D Ramp Leasehold and the Taxiway Alpha Non-movement Line.

We strongly recommend that all operators check the daily Distant NOTAMS and VEOCI mass web e-mails. Your cooperation is appreciated throughout this construction project and if you have any questions, please contact Airport Operations at (914) 995 - 4850.

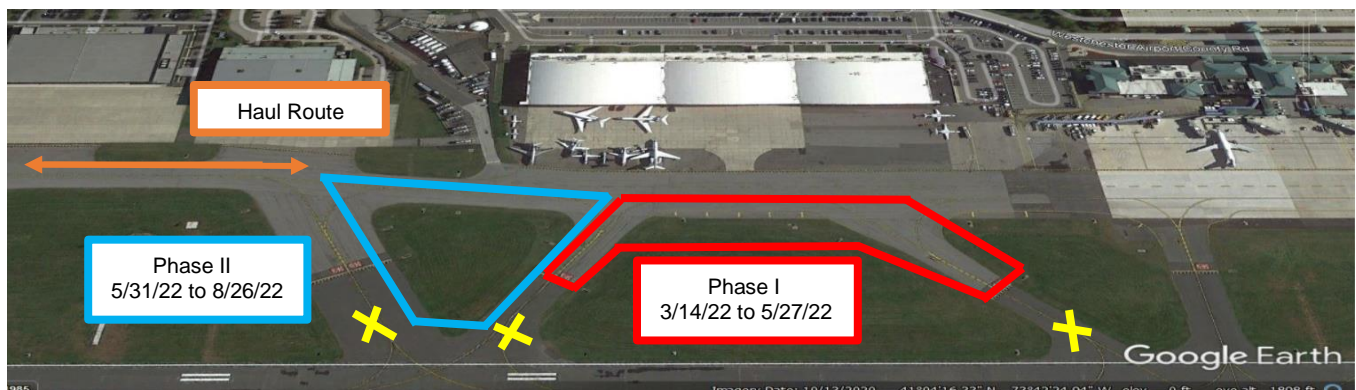

John Starace
Airport Operations Manager
