


April 2022

Peachtree Corners Public Works Project Roundup

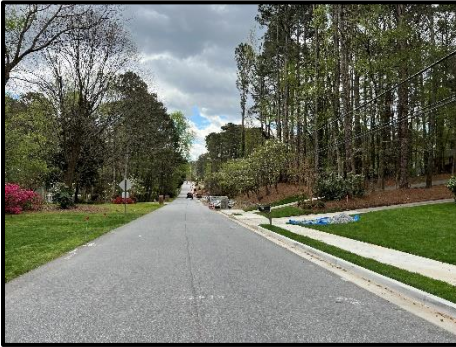

Gunnin Road Sidewalks

- Overview - Sidewalks on the west side of Gunnin Road from Spalding Drive to Willbanks Drive.
- Update - Construction has been delayed due to supply shortages, construction schedules, and the impact of COVID.
- Scheduled Completion – Spring 2022

Local Maintenance and Improvement Grant Sidewalk Program

- Overview - Sidewalks on the east side of Jones Mill Road from Green Pointe Parkway to Peachtree Corners Circle, both sides of Peachtree Corners Circle from Peachtree Industrial Blvd to Jones Mill Spur, and Engineering Drive from SR 141 to the next driveway setting up for a future trail opportunity. The project also includes a speed table on Town Center Boulevard
- Update - Project nearing completion.
- Scheduled Completion – Spring 2022



Bush Road and Medlock Road

- Overview - Intersection improvement of Bush Road and Medlock Bridge Road. The project adds an extra through lane on Medlock Bridge Road and an additional slip lane from Bush Road onto SR 141/Peachtree Parkway.
- Update - Construction is underway but had a delay because of utilities and the delivery of the joint use pole being delayed. The project was also delayed due to a Gwinnett County revision. Both issues have been resolved and construction should be ramping back up soon.
- Scheduled Completion - Summer of 2022.



Town Center Corners Connector

- Overview – Added trail adjacent to Town Center connecting Peachtree Corners Circle, Town Center, the adjacent shopping plaza, the Pedestrian Bridge, and SR 141.
- Update – Construction ongoing
- Scheduled Completion – Summer 2022

Bankers Industrial Bioretention and Stormwater Installation

- Overview - The project will install 10 linear Bioretention cells/bioswales totaling up to 13,00 square feet along Bankers Industrial Drive
- Update - Currently under utility relocation. The contractor will start immediately upon completion.
- Scheduled Completion – Summer 2022



Town Center Enhancements

- New playground at Town Center including walls sidewalks and shade structures
- Construction is underway. Drainage lines have been installed. Grading is ongoing. Soil testing for the playground foundation is underway.
- Scheduled Completion – Summer 2022



Spalding Drive Widening

- Spalding Drive Widening from Winters Chappel Road to Holcomb Bridge Road and includes the widening of the bridge over Crooked Creek.
- Construction is underway but had a slight delay in April 2021. The issues were resolved in June 2021 and construction is ongoing.
- Scheduled Completion – Fall 2022



East Jones Bridge Riverlands Trail

- Overview - A 10- to 12-foot-wide multi-use trail on the east side of East Jones Bridge Road from SR 141 to Jones Bridge Park.
- Update – The project is underway and moving. It starts at SR 141 heading north. Some adjustments and stormwater revisions are located near Broadgreen.
- Scheduled Completion – Fall 2022
