


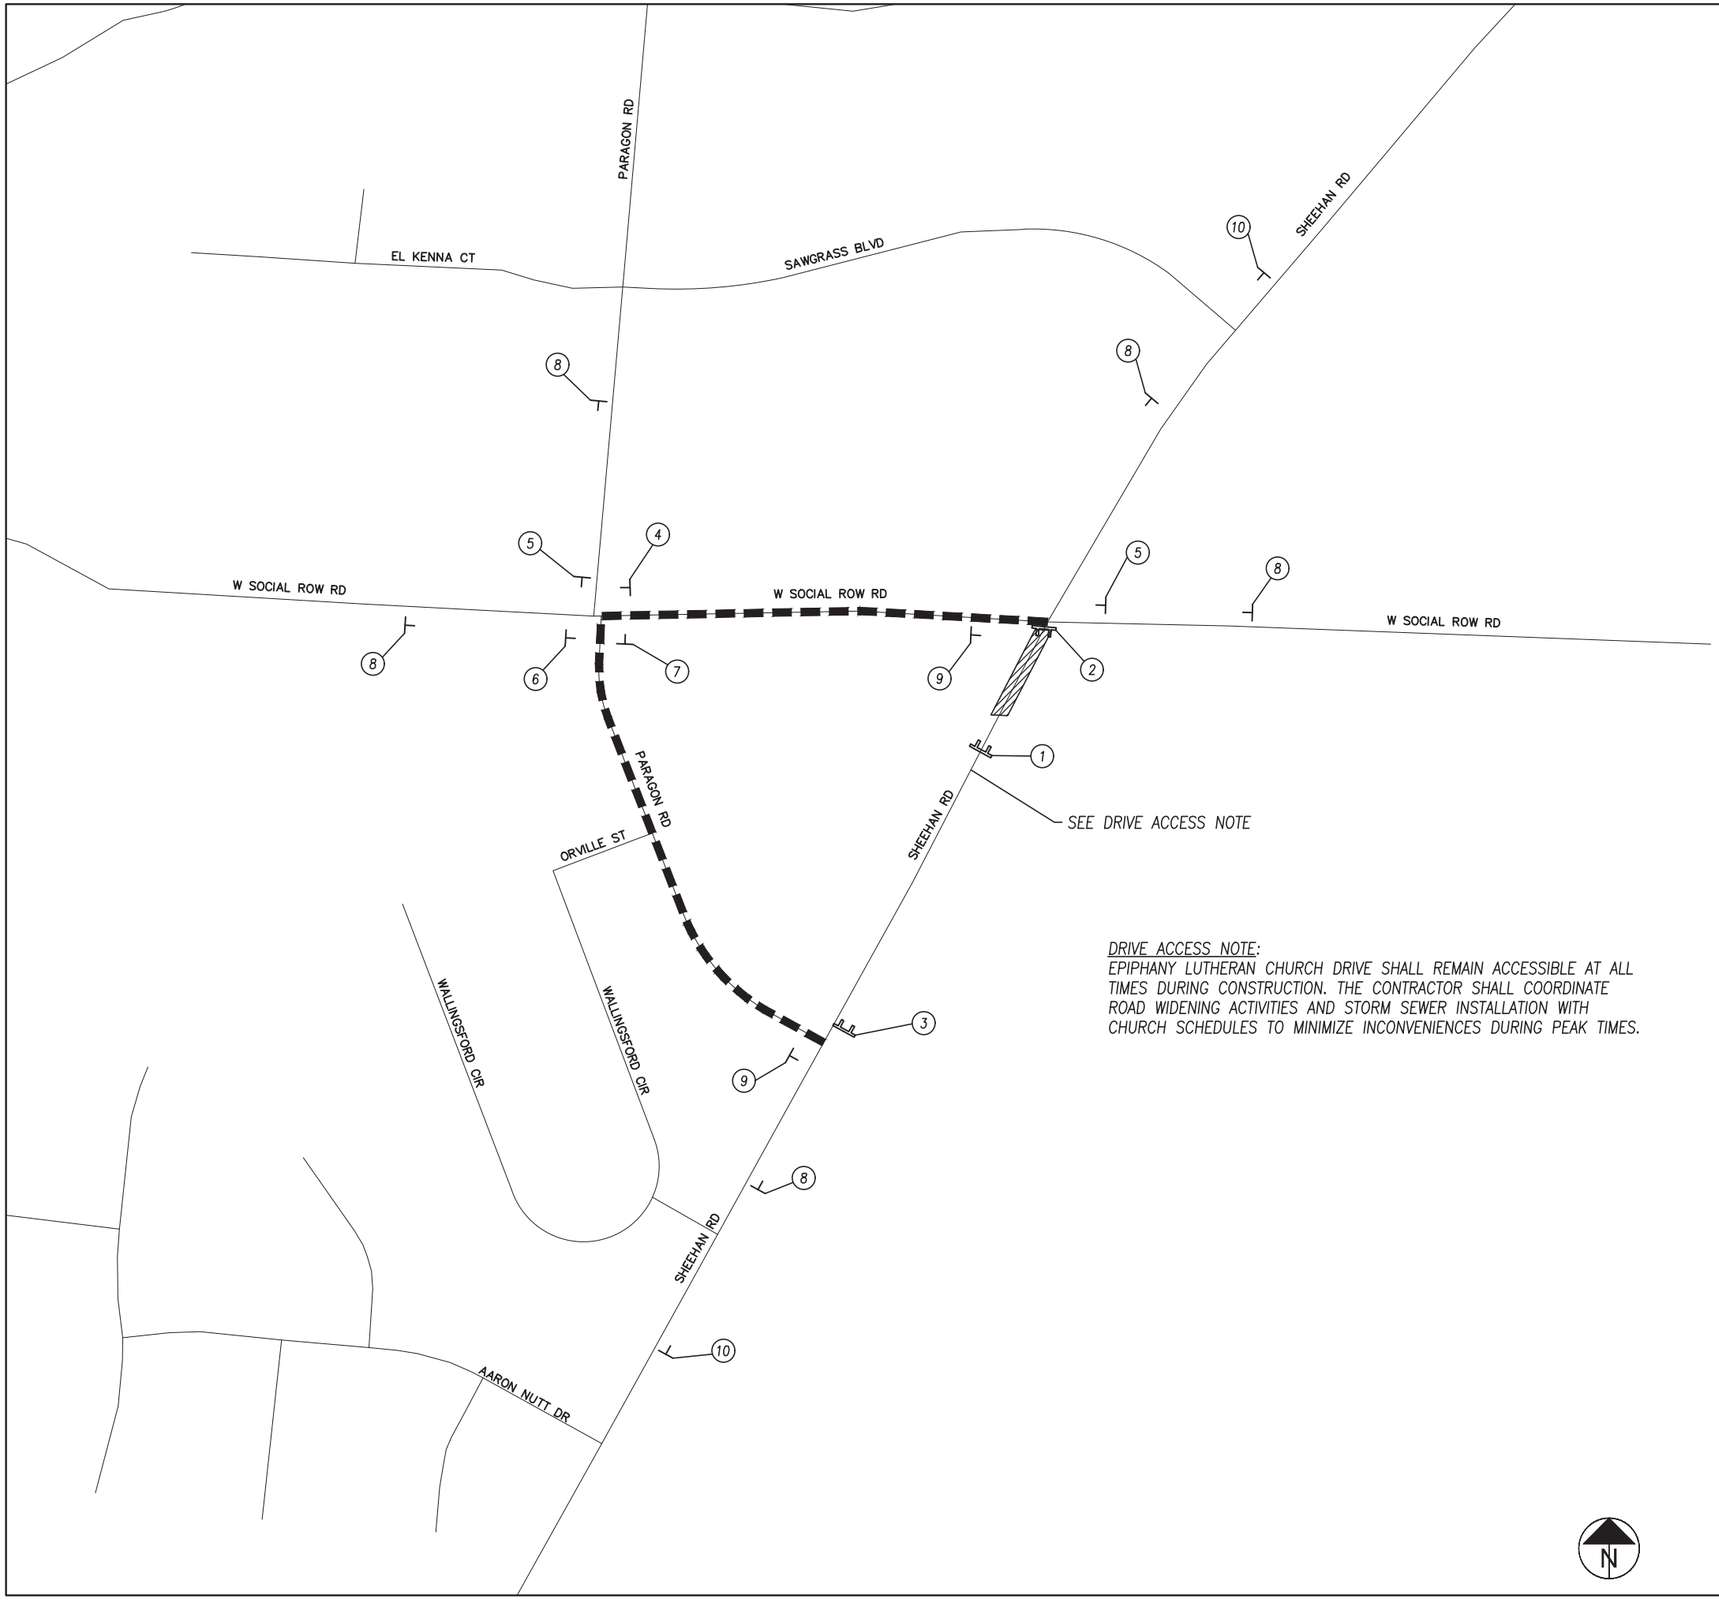


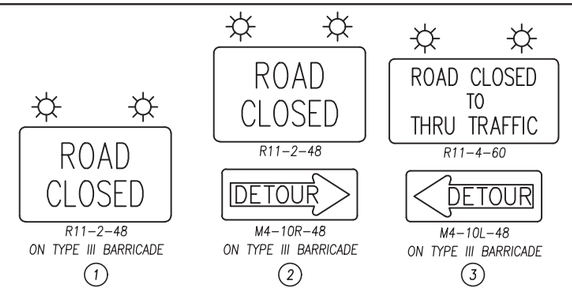





DRIVE ACCESS NOTE:
EPIPHANY LUTHERAN CHURCH DRIVE SHALL REMAIN ACCESSIBLE AT ALL TIMES DURING CONSTRUCTION. THE CONTRACTOR SHALL COORDINATE ROAD WIDENING ACTIVITIES AND STORM SEWER INSTALLATION WITH CHURCH SCHEDULES TO MINIMIZE INCONVENIENCES DURING PEAK TIMES.

LEGEND:

- *DETOUR ROUTE*
- *WORK AREA*

NOTES:

- *THE CONTRACTOR SHALL PROVIDE, ERECT, MAINTAIN, AND REMOVE THE DETOUR SHOWN. PAYMENT FOR ALL LABOR, EQUIPMENT, AND MATERIALS NECESSARY TO PERFORM THIS WORK SHALL BE INCLUDED IN THE LUMP SUM BID FOR ITEM 614 – DETOUR SIGNING.*
- *IN ADDITION TO THE TRAFFIC CONTROL REQUIREMENTS SHOWN ON THIS SHEET, THE TRAFFIC CONTROL REQUIREMENTS SHOWN ON S.C.D. MT–101.60 SHALL ALSO APPLY.*

CALCULATED ELV | CHECKED JRM

DETOUR PLAN - PHASE 2B - SHEEHAN ROAD SOUTH OF SOCIAL ROW ROAD

MOT-CR166-8.13
MOT-SOCIAL ROW ROAD

01/24/2025
