

Medfield State Hospital Redevelopment

Trinity Financial Presentation to the *Town of Medfield Select Board*

February 6, 2024

Order of Discussion

- 2023 Milestones & 2024 Goals
- Anticipated Timeline to Closing
- Town Support



2023 Milestones & 2024 Goals

Additions to the Trinity Team

- **Dan Moore**
  - Hired in the Summer of 2023 as Construction Manager for MSH Project
  - 25 years of experience in the construction industry and on Trinity projects
  - Oversaw on-site exploratory efforts for MHC/NPS, coordination with Eversource, and outreach to Longmeadow/Evergreen neighborhood residents
  - Lives in Walpole, MA

- **Greg Lane**
  - Public Affairs Advisor at Next Generation Strategies
  - Oversees communications and public processes for complex, transformative development projects
  - Developing media and public outreach strategy to keep the Medfield community informed of progress

Critical Path Items to Closing


- State and Federal Historic Part II Approval
- Allocation of State Historic Tax Credits
- Extraordinary cost funding for public infrastructure and hazardous materials remediation




State Grants Received for MSH Redevelopment

- **Anticipated since TFI submission of the MSH RFP Response**
- **Public Infrastructure**
  - 9,200 linear feet (LF) of public roadways and subsurface utilities for TFI & Bellforge Arts Center
  - **TFI retained Anderson Strategic Advisors for submission of state grant funding**
  - **Town received HousingWorks Infrastructure Grant for $4,486,800, September 2023.**
  - Scope of Work:
    - VHB Design of Public Infrastructure
    - 1,200LF Sewer Extension to serve MSH Property
    - Improvement of three, off-site vehicular intersections leading to Hospital Road
- **Extraordinary Site Remediation**
  - Remediation of lead, asbestos, and other hazardous materials present in the existing 27 buildings
  - **TFI retained Anderson Strategic Advisors for submission of state grant funding**
  - **Town received Underutilized Properties Grant for $500,000, September 2023.**
  - Scope of Work:
    - Inspection of asbestos-containing materials, OSHA lead-based paint, and regulated materials in all 27 buildings
    - Selective remediation and demolition in Building 6

Off-site Improvements

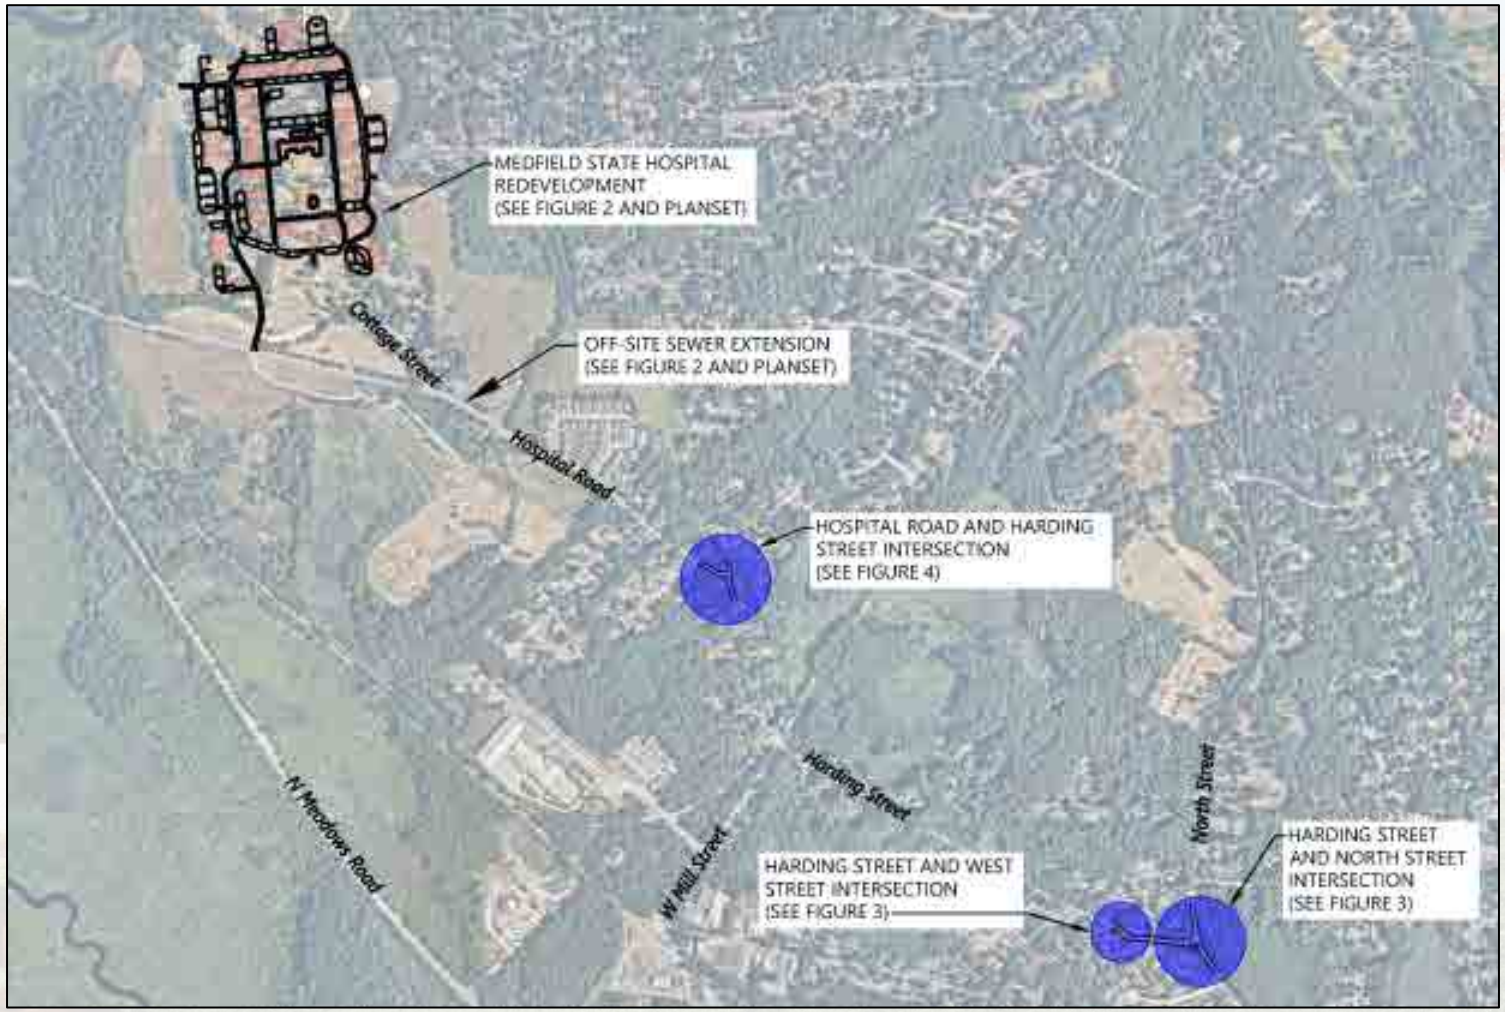


1,200LF Sewer Extension on Hospital Road

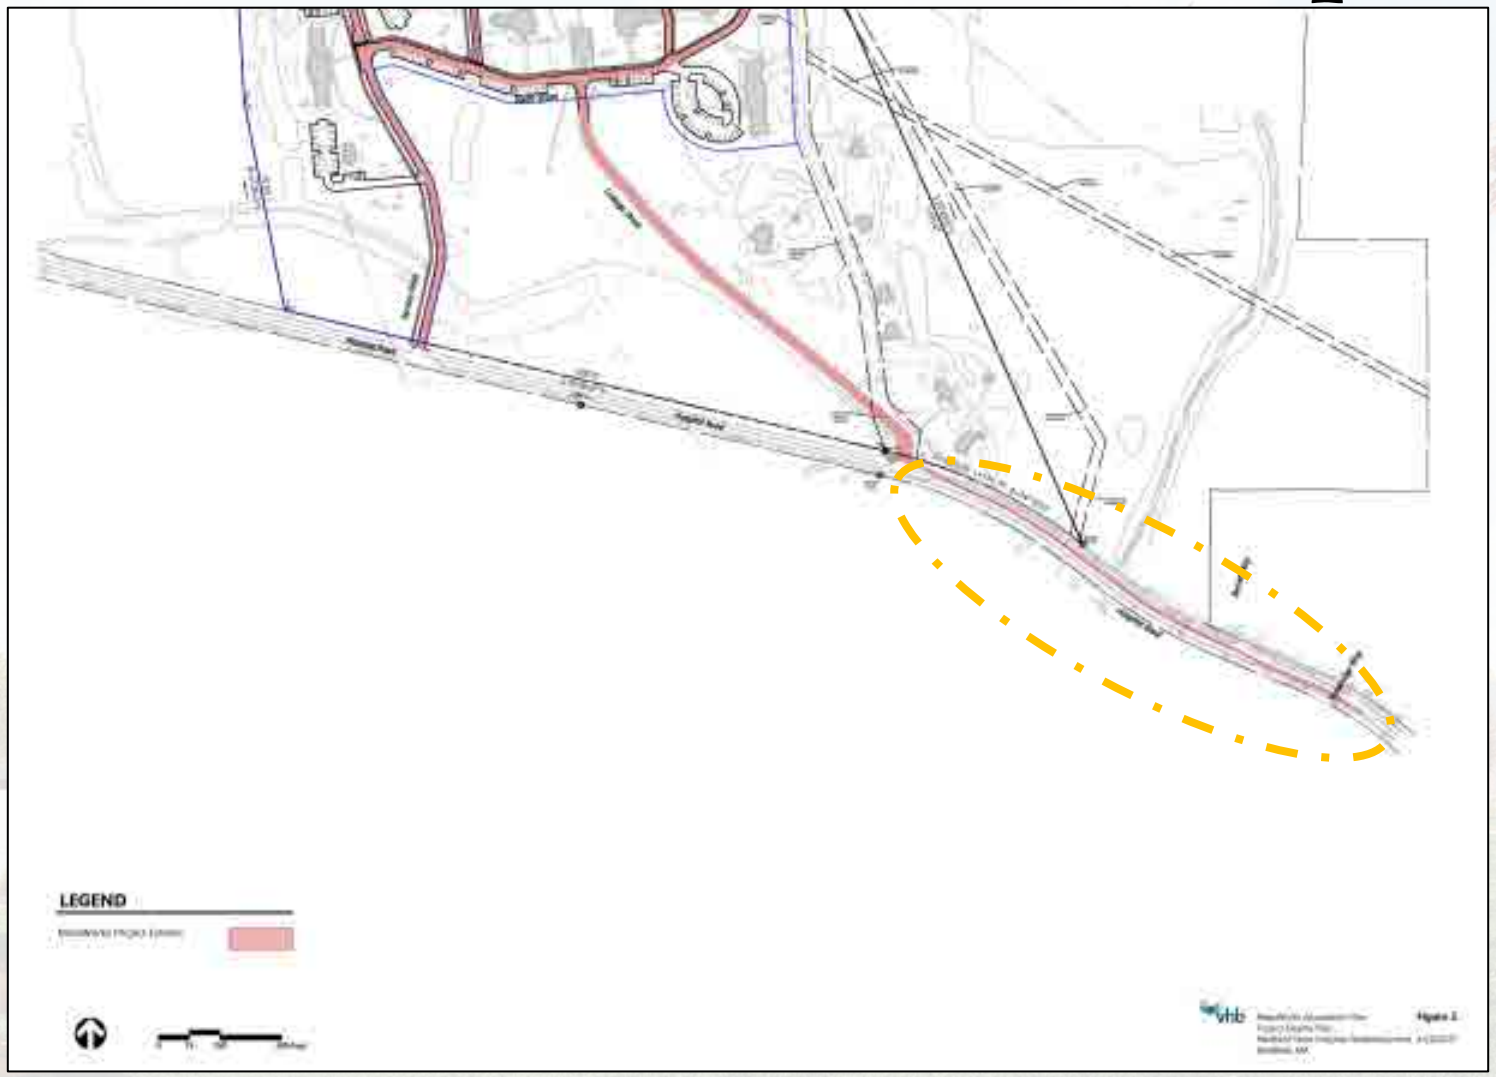


Harding Street at West and North Streets



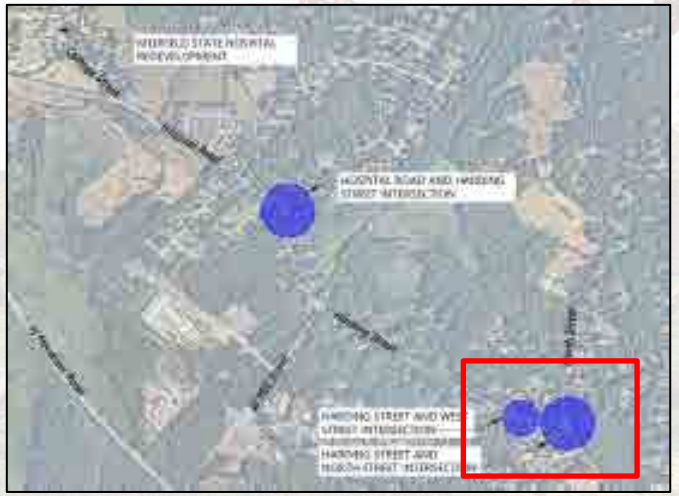


Harding Street at West and North Streets



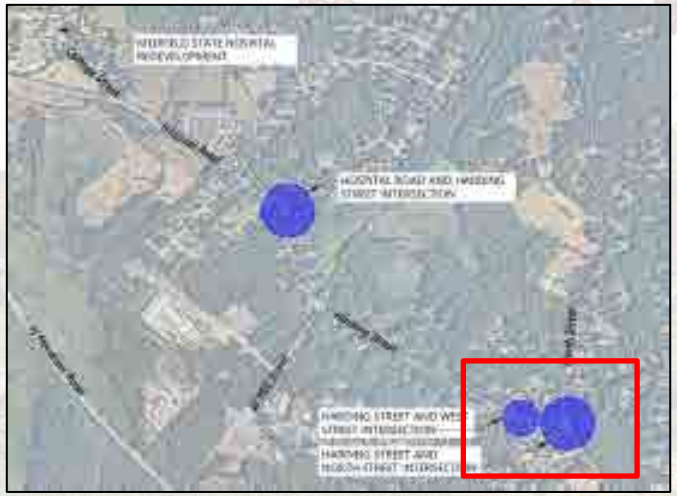


Harding Street at Hospital Road



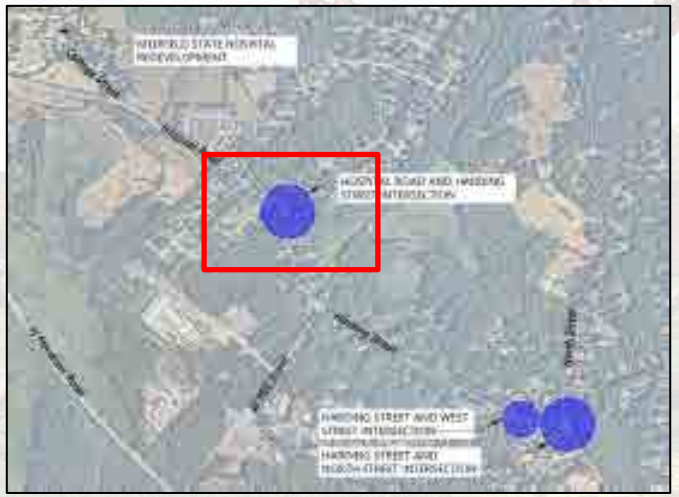

Harding Street at Hospital Road



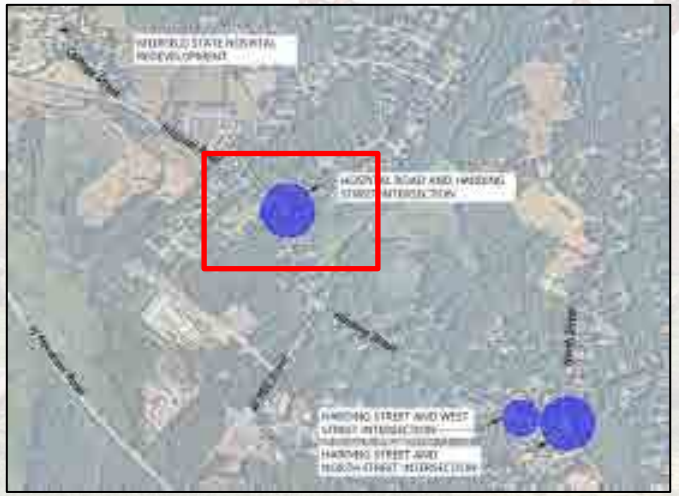

Permitting in 2023 – 75% Complete

- Conditional Site Plan Approval from the Medfield Planning Board
- MEPA Notice of Project Change
- Completed Tree Survey

Permitting 2024 – Goal: 100% Complete

- VHB Design of Public Infrastructure
  - Part of HWIP Scope of Work
  - Accessibility ramps and mechanical equipment need NPS/MHC approval
- Final Site Plan Approval and Subdivision Plan Approval from the Medfield Planning Board
- MEPA Single Environmental Impact Report



Historic & Design in 2023

Spring 2023


- Submitted Part II Application to the National Park Service (NPS)

Fall 2023

- Submitted 1st round of 27 separate applications for State Historic Tax Credits (HTCs) to Massachusetts Historical Commission (MHC)
- Received comments and clarifications from NPS/MHC

Winter 2023

- Authorized architects on exploratory work and 25% Design Development
- Submitted 700+ page NPS clarification package
- Submitted 2nd application for State HTCs to MHC

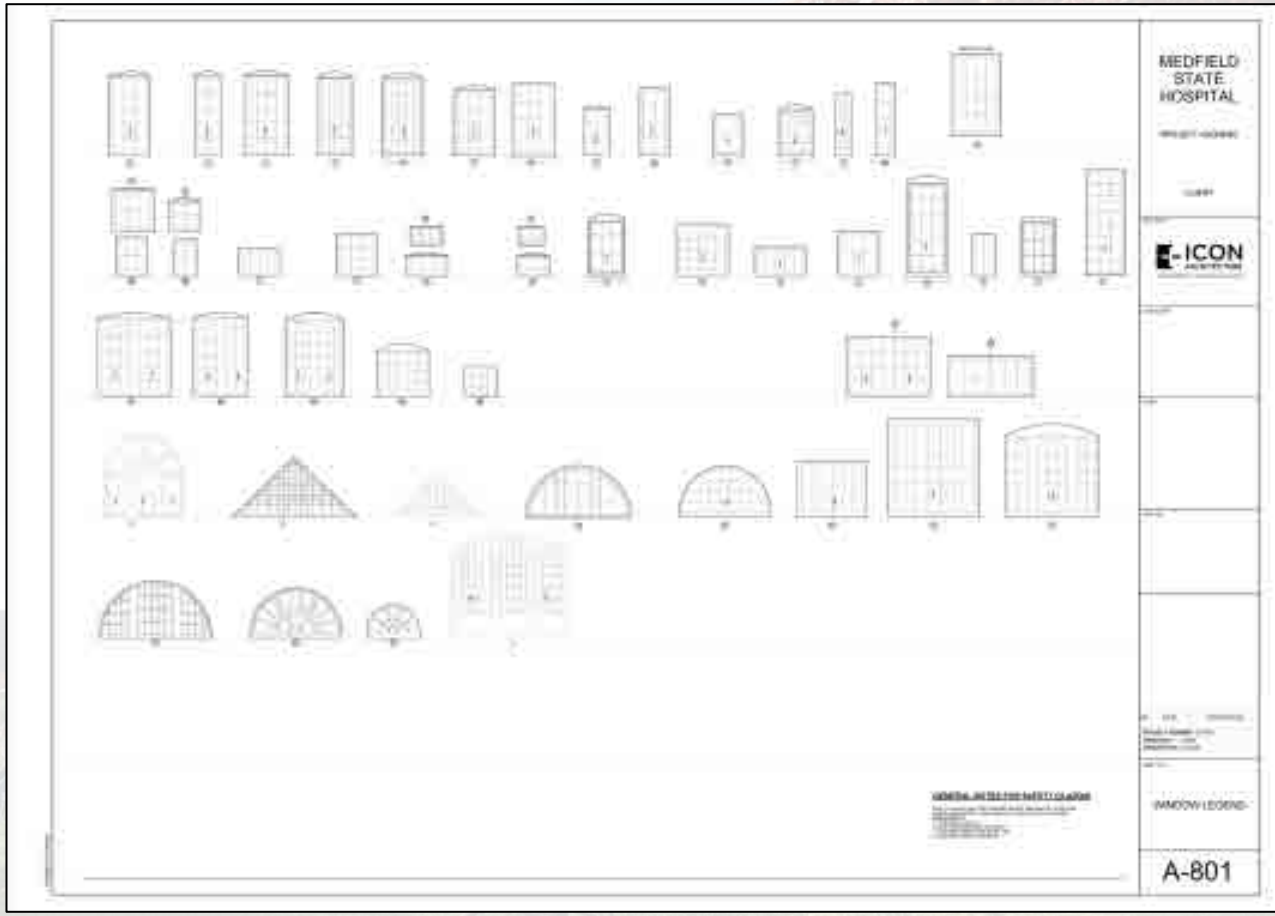

Historic & Design in 2024

Spring 2024

- 3rd application for State HTCs to MHC
- Anticipated final comments/questions from NPS/MHC
- NPS/MHC Part II Approval

Fall 2024

- 4th application for State HTCs to MHC



Financing in 2023

- Engaged with numerous state offices and elected officials about the importance of the project and exploring alternative avenues for financing
  - Hosted group tours of the MSH Site for maximum impact
- Updated accountants and historic tax credit investors on residential development financial structure
  - CohnReznick
  - Bank of America
  - Chase Bank



Financing in 2024

Spring/Summer 2024

- Support Town of Medfield with second OneStop application for public infrastructure and hazardous materials remediation funding
- Engage with lenders and private equity investors

Anticipated Timeline to Closing

Anticipated Timeline to Closing

- Change in Governor Administration in 2023 resulted in changes in the agencies governing the necessary financing for the project
- NPS/MHC process is taking longer than anticipated due to the sheer volume of materials they need to review and comment on
- Trinity has engaged with Town Boards, State Delegation, Agency Secretaries, and the Healey/Driscoll Administration
  - All parties are supportive; Valued Historic Asset
  - Creative solutions for the infrastructure and remediation funding necessary due to the Commonwealth abandoning the property for 50+ years



WHEN public infrastructure and remediation funding is secured, the project could close as soon as 9-12 months from commitment.

Continued Partnership

Continued Partnership

- TFI Weekly check-ins with Government Affairs Consultants
- Bimonthly Calls with Town Staff
- Facilitate Monthly Updates to the Medfield Community in the Town Administrator's Letter
- TFI Monthly Coordination with Bellforge Arts Center
- TFI Predevelopment expenditures $1.5M+
- Oversight of the HWIP/UPP Grant 1st Phase of work
- Approval of the second submission to OneStop for second round HWIP/UPP funding
- Letters of support for MHC/NPS submissions
- MBTA Communities Compliance
- Extension of the LDA to allow for sufficient funding for infrastructure and remediation





Questions & Comments
